

CITY OF NEWPORT BEACH ADMINISTRATIVE HEARING STAFF REPORT

February 20, 2025 Agenda Item No. 2

SUBJECT:	Three-Year Construction Time Limit Extension in Accordance with Newport Beach Municipal Code (NBMC) 15.02.095 (Addition of Sections 105.3.3, 105.3.4 and 105.3.5), Section 105.3.4, Item 2
PERMITS:	X2019-2085, U2024-5306
SITE LOCATION:	914 E. Ocean Front
APPLICANT:	Ron Carroll
PROPERTY OWNER:	Ocean Property Rentals LLC
BUILDING INSPECTOR:	Jason Rudenick, Senior Building Inspector
PREPARED BY:	Tonee Thai, Chief Building Official - 949-718-1867, <u>tthai@newportbeachca.gov</u>

PROJECT SUMMARY

NEW 2,617 SF SINGLE-FAMILY DWELLING WITH 484 SF GARAGE, 135 SF BALCONY, 460 SF ROOF DECK AND 640 SF ROOF LOGGIA.

BUILDING PERMIT HISTORY

This project first started with Permit X2019-2085 issued on October 14, 2020. The referenced permits above are subject to Newport Beach Municipal Code 15.02.095 with initial three-year construction limit expiration date of October 14, 2023.

Permit U2024-5306 is a supplement permit to construct site block wall.

The first inspection was on October 26, 2020, for a Pre-Grading Meeting.

The last inspection was on September 27, 2024, for Final Building Inspection.

Please refer to Attachment 1 for detailed permit history.

Notice of pending Three-Year Construction Limit expiration were sent on July 28, 2023.

Please refer to Attachment 2 for detailed notice activities.

BUILDING OFFICIAL EXTENSION

The chief building official granted a total of 365 days extension for a three-year construction time limit, with an expiration date of October 13, 2024. (Attachment 3).

RECOMMENDATION

- 1) Conduct a public hearing;
- Find this project exempt from the California Environmental Quality Act (CEQA) pursuant to Section 15301 under Class 1 (Existing Facilities) of the CEQA Guidelines, because this project has no potential to have a significant effect on the environment;
- 3) The hearing officer may grant, or conditionally grant, up to a 180-calendar day extension, per application for extension, if the officer finds special circumstances warrant an extension of time, or the failure to meet the time limit was caused by circumstances beyond the property owner, applicant, or the contractor's control. If the officer makes the findings to grant an extension, then the officer shall consider whether conditions are necessary to ensure the timely completion of the project in a manner that limits impacts to the surrounding property owners. The hearing officer shall deny the application if they cannot make the findings set forth in Newport Beach Municipal Code Section 15.02.095 (Addition of Sections 105.3.3, 105.3.4, and 105.3.5).

PUBLIC NOTICE

Notice of this hearing was published in the Daily Pilot, mailed to all owners of property within 300 feet of the boundaries of the site (excluding intervening rights-of-way and waterways) including the applicant, and posted on the subject property at least 10 days before the scheduled meeting, consistent with the provisions of the Municipal Code. Additionally, the item appeared on the agenda for this meeting, which was posted at City Hall and on the city website.

ATTACHMENTS

Attachment No. 1 – Building Permit History Attachment No. 2 – Three-Year Construction Limit Notice Activities Attachment No. 3 – Building Official Extension

Attachment No. 1

Building Inspection History



LINKED PERMIT INSPECTION HISTORY REPORT (1519-2019) FOR CITY OF NEWPORT BEACH

Permit Type:	Plan Check	Application Date:	07/03/2019	Owner:	
Work Class:	New	Issue Date:	10/14/2020	Parcel	048 143 19
Status:	Approved	Expiration Date:	12/30/2020	Address:	914 E OCEAN FRONT
IVR Number:	133749				NEWPORT BEACH, CA

Scheduled Date	Actual Start Date	Inspection Type	Inspection No.	Inspection Status	Primary Inspector	Reinspection Required?	Complete
Inspection L	ocation: 914 C	DCEAN FRONT E					
Permit: E202	0-0569						
11/17/2020	11/17/2020	Legacy Inspection	E2020-0569-A0027 63799	Approved	Steven Lane	No	Complete
	11/17/2020	Temporary Power Pole	E2020-0569-A0027 63798	Approved	Steven Lane	No	Complete
Permit: H202	1-0538						
02/16/2022	02/16/2022	Other - MISC	H2021-0538-A0029 45493	Approved		No	Complete
Permit: N202	0-0645						
11/05/2020	11/05/2020	Rough Utilities	N2020-0645-A0027 60252	Partial Pass		No	Incomplete
11/06/2020	11/06/2020	Rough Utilities	N2020-0645-A0027 60723	Partial Pass	Kiel Wilcox	No	Incomplete
12/11/2020	12/11/2020	Excavation	N2020-0645-A0027 73204	Partial Pass	Robert Silva	No	Incomplete
01/25/2021	01/25/2021	Public Works Inspection	N2020-0645-A0027 85795	Partial Pass	Kiel Wilcox	No	Incomplete
01/26/2021	01/26/2021	Service Connections - Utilities	N2020-0645-A0027 86208	Partial Pass		No	Incomplete
	01/26/2021	Sewer Clean-Out	N2020-0645-A0027 86206	Approved		No	Complete
	01/26/2021	Sewer Lateral	N2020-0645-A0027 86207	Approved		No	Complete
Permit: U202	4-5306						
09/27/2024	09/27/2024	Footings and Foundation	iBLD-037825-2024	Approved	Jason Rudenick	No	Complete
	09/27/2024	Masonry Pre-Grout	iBLD-037826-2024	Approved	Jason Rudenick	No	Complete
Permit: X201	9-2085						
10/26/2020	10/26/2020	Call Inspector for Pre-Grade Meeting	X2019-2085-A0027 55731	Partial Pass	Walter Jones	No	Incomplete
11/23/2020	11/23/2020	Soil Pipe	X2019-2085-A0027 66398	Approved		No	Complete
12/03/2020	12/03/2020	Call Inspector for Pre-Grade Meeting	X2019-2085-A0027 69892	Approved	Walter Jones	No	Complete
	12/03/2020	Erection Pads	X2019-2085-A0027 69897	Approved	Walter Jones	No	Complete
	12/03/2020	Legacy Inspection	X2019-2085-A0027 69901	Approved	Walter Jones	No	Complete
	12/03/2020	Rough Grade Approval	X2019-2085-A0027 69893	Approved	Walter Jones	No	Complete

LINKED PERMIT INSPECTION HISTORY REPORT (1519-2019)

Permit Type:	Plan Check	Application Date:	07/03/2019	Owner:	
Work Class:	New	Issue Date:	10/14/2020	Parcel	048 143 19
Status:	Approved	Expiration Date:	12/30/2020	Address:	914 E OCEAN FRONT
IVR Number:	133749				NEWPORT BEACH, CA

Scheduled Date	Actual Start Date	Inspection Type	Inspection No.	Inspection Status	Primary Inspector	Reinspection Required?	Complete
	12/03/2020	WQ-Best Management Practices	X2019-2085-A0027 69896	Partial Pass	Walter Jones	No	Incomplete
02/01/2021	02/01/2021	Footings and Foundation	X2019-2085-A0027 89117	Correction	Walter Jones	No	Complete
02/02/2021	02/02/2021	Footings and Foundation	X2019-2085-A0027 89239	Approved	Walter Jones	No	Complete
	02/02/2021	Ufer Ground	X2019-2085-A0027 89237	Approved	Walter Jones	No	Complete
02/09/2021	02/09/2021	Slab On Grade	X2019-2085-A0027 92925	Approved	Walter Jones	No	Complete
03/31/2021	03/31/2021	Floor Framing & Sheathing	X2019-2085-A0028 13481	Partial Pass	Walter Jones	No	Incomplete
05/11/2021	05/11/2021	Floor Framing & Sheathing	X2019-2085-A0028 29828	Partial Pass	Walter Jones	No	Incomplete
09/27/2021	09/27/2021	Floor Framing & Sheathing	X2019-2085-A0028 88239	Approved		No	Complete
	09/27/2021	Roof Framing, Sheathing, Building Height	X2019-2085-A0028 88240	Approved		No	Complete
	09/27/2021	Shear and Hold Downs	X2019-2085-A0028 88241	Approved		No	Complete
01/13/2022	01/13/2022	Fireplace Throat	X2019-2085-A0029 31069	Approved		No	Complete
	01/13/2022	Gas Pipe Underground	X2019-2085-A0029 31066	Approved		No	Complete
	01/13/2022	Hood	X2019-2085-A0029 31068	Approved		No	Complete
	01/13/2022	HVAC	X2019-2085-A0029 31067	Approved		No	Complete
	01/13/2022	ZZZPlumbing	X2019-2085-A0029 31065	Approved		No	Complete
01/27/2022	01/27/2022	Complete Framing	X2019-2085-A0029 36825	Approved		No	Complete
	01/27/2022	Rough Electrical Service	X2019-2085-A0029 36824	Approved		No	Complete
02/15/2022	02/15/2022	Rough Electric Residential	X2019-2085-A0029 45036	Approved		No	Complete
03/18/2022	03/18/2022	Legacy Inspection	X2019-2085-A0029 59497	Approved		No	Complete
06/01/2022	06/01/2022	Insulation/Densglass	X2019-2085-A0029 92147	Partial Pass		No	Incomplete
	06/01/2022	Insulation/Densglass	X2019-2085-A0029 92148	Approved		No	Complete
06/14/2022	06/14/2022	Drywall Fire Caulk	X2019-2085-A0029 97722	Approved		No	Complete

LINKED PERMIT INSPECTION HISTORY REPORT (1519-2019)

Permit Type:	Plan Check	Application Date:	07/03/2019	Owner:	
Work Class:	New	Issue Date:	10/14/2020	Parcel	048 143 19
Status:	Approved	Expiration Date:	12/30/2020	Address:	914 E OCEAN FRONT
IVR Number:	133749				NEWPORT BEACH, CA

Scheduled	Actual					Reinspection	
Date	Start Date	Inspection Type	Inspection No.	Inspection Status	Primary Inspector	Required?	Complete
06/30/2022	06/30/2022	Shower Lath	X2019-2085-A0030 04753	Approved		No	Complete
Permit: X202	0-2304						
10/26/2020	10/26/2020	Final Building	X2020-2304-A0027 55734	Approved	Walter Jones	No	Complete
	10/26/2020	Final Plumbing	X2020-2304-A0027 55733	Approved	Walter Jones	No	Complete
	10/26/2020	Sewer	X2020-2304-A0027 55732	Approved	Walter Jones	No	Complete
nspection Lo	ocation: 914 C	DCEAN FRONT E A					
Permit: X201	9-2085						
07/20/2023	07/20/2023	Gas Pressure Test	iBLD-027393-2023	Approved	Jason Rudenick	No	Complete
09/14/2023	09/14/2023	WQ-Best Management Practices	iBLD-035505-2023	Partial Pass	Jason Rudenick	Yes	Incomplete
04/02/2024	04/02/2024	Other - Plumbing	iBLD-012567-2024	Approved	Jason Rudenick	No	Complete
05/08/2024	05/08/2024	Final Electrical	iBLD-017874-2024	Partial Pass	Jason Rudenick	Yes	Incomplete
09/27/2024	09/27/2024	Final Building	iBLD-037827-2024	Partial Pass	Jason Rudenick	Yes	Incomplete

City of Newport Be 100 Civic Center Drive, Newport Permit Counter Phone (949)64 Inspection Requests Phone (9 Combination Type - SFP G	ort Beach, CA 92660 14-3288 149)644-3255 IRAD ELEC MECH PLU		X 2 Ø 1 9 2		F Is Ir ED BY 10/15/2023 (Project No : 15 ssued Date : 10/14 hspection Area : DR PERMIT WILL	1/2020 1 BE INVALID	
Job Address: 914 E OCEAN FRONT NB Description: NEW SFR W/GAR 2617 & 484 SF, I Legal Desc.: BALBOA TR BLK 14 LOT 22	onday - Friday 7:00 a.m.	to 6:30 p.m.	and Saturday from 8:00	a.m. to 6:00	i p.m. No work of	i Sunuays or n	olidays TION WORK	
Owner: ATALL PAYAM CHARLES	Contractor:	CARROL	L RONALD L GEN CONTRA	CTORS INC	Architect:			
Address: 24881 ALICIA PKWY #G LAGUNA HILLS CA 92653 Phone: 949-637-1332	Address: Phone:	P O BOX HUNTING 714-749-6	STON BEACH CA 92615	Address: Phone:		N SATUR State Lic:	IDAYS	
Applicant:JEHEBER RODAddress:410 32ND ST #202NEWPORT BEACH CA 92663Phone:949-723-4393	Con State Lic: Lic Expire: Bus Lic: Lic Exp Date:	10/31/202 BT30069	597	Engineer: Address: Phone:	REZAEI ALI 18021 SKYPARK IRVINE CA 92614 949-466-9394		1068	
Code Edit :2016Type of Construction:V-B-SPROccupancy Group:R-3/UAdded /New sq.ft. Bldg:2617	Worker's Compensa Carrier: Policy No: Expire:	ation Insuranc W/C EXE (NO EMP	MPT	Designer: Address: Phone:	JEHEBER ROD 410 32ND ST #203 NEWPORT BEAC 949-723-4393	2 H CA 92663		
Added /New sq. ft. Garage: 484 No of Stories: 3 No of Units : 1 Bldg Height: 0 Bldg Sprinklers: Y	Building Setbacks	Rear: 0 Front: 6' Left: 3' Right: 3'		Special Cond	ditions: HIGH DENS LIQUEFACT 4BR -> 4 BF		SPECTO	R
Flood Zone: 0.2% Construction Valuation: \$535,200.00	Use Zone: F	Parking Space	s: 0	I lie Hazaru	Zone : N			
Construction Valuation:\$535,200.00Building Permit Fee:\$5,840.00Plan Check Fee:\$3,338.50Overtime Plan Ck:\$0.00Investigation Fee:\$0.00Record Management :\$108.00Energy Compliance:\$303.00CA Seismic Safety :\$69.58Disabled Access :\$0.00Hazardous Mat\$0.00Building Green Fee :\$22.00	Additional Fee : Grading Bonds Fee: Grading PC Consultant : Grading PC Fee: WQ Insp. Fee : Electrical %:	\$651.21 \$63.00 \$0.00 \$774.08 \$952.00 \$998.16 \$120.00 \$408.80 \$233.60 \$525.60	San Dist : NMUSD Fee: \$	\$46 \$ \$ nent - \$0.00 \$344.00 \$0.00 1,251.20	2.50 Fire 0.00 Fire P 0.00 Demo 0.00 Bui Gen Ref Grad	epartment Inspection: Ian Rev litton Fee ding Dept Adm neral Service und Deposit ing Bond:	\$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00	
TOTAL FEE: \$16,465.23		Plan Check	Fee:\$4,717.25 🚬	See D	ue, at, Permit Issu	iance :	\$11,747.98	
PROCESSED BY: ZONING APPROVAL: GRADING APPROVAL:	B Sen		PUBLIC WO PLAN CHEC APPROVAL	- 	ÿAL ² ²	lodi UTO	7	

_· _ \$,							
OWNER-BUILDER D	ECI ARATION						
I hereby affirm under per (Section 7031.5, Business a the permit to file a signed sta Professions Code) or that he not more than five hundred of	halty of perjury that I am e nd Professions Code: Any atement that he or she is i or she is exempt from lic dollars (\$500).	xempt from the Contractors' State Lid y city or county that requires a permit licensed pursuant to the provisions of censure and the basis for the alleged	to construct, alter the Contractors' s exemption. Any vi	, improve, demol State License La olation of Section	lish, or repair any structu w (Chapter 9 (commenc n 7031.5 by any applicar	rre, prior to its issuance, ais ing with Section 7000) of Di nt for a permit subjects the a	vision 3 of the Business and upplicant to a civil penalty of
Business and Professions C improvements are not intend improved for the purpose of	ode: The Contractors' Sta led or offered for sale. If, sale).	wages as their sole compensation, w the License Law does not apply to an however, the building or improvemen	owner of property it is sold within on	who, through en e year of comple	ployees' or personal eff tion, the Owner-Builder	fort, builds or improves the p will have the burden of provi	ng that it was not built or
apply to an owner of propert	y who builds or improves	cting with licensed Contractors to con thereon, and who contracts for the pr	ojects with a licen	Section 7044, B sed Contractor p	usiness and Professions ursuant to the Contracto	s Code: The Contractors' Sta ors' State License Law).	ate License Law does not
By my signature below I ack sell a structure that I have be Professions Code, is availab Signature of Property Owner	nowledge that, except for uilt as an owner-builder if le upon request when this or Authorized Agent	' State License Law for the following my personal residence in which I mu it has not been constructed in its enti application is submitted or at the fol	st have resided fo rety by licensed co	ontractors. I unde	erstand that a copy of th	the improvements covered e applicable law, Section 70 Date	by this permit, I cannot legally 44 of the Business and
U OFNOED CONTRACTO	NDIO DECLADATION	sed under provisions of Chapter 9 (co		action 7000) of I	Division 2 of the Bucieor	and Professiona Fords an	d my license is in full force
I hereby affirm under penalty and effect License Class	of perjury that I am licen	License No	statiencing with S	_ Date // 142	-14-20 Contractor	Signature	
WORKERS' COMPENSA	TION DECLARATION					y .	-
MADAINO, FAU UPE TO SECURE V	ODVERS' COMPENSATION CO	VERAGE IS UNLAWFUL, AND SHALL SUBJECTION 3706 OF THE LABOR CODE, INTEREST, A	T AN EMPLOYER TO	CRIMINAL PENALTIE S.	ES AND CIVIL FINES UP TO O	NE HUNDRED THOUSAND DOLLA	RS (\$100,000), IN ADDITION TO THE
I hereby affirm under penalty	of perjury one of the follo	wing declarations:					
I have and will maintain performance of the work for	a certificate of consent which this permit is issued	to self-insure for workers' compens d. Policy No.	ation, issued by 1	the Director of I	ndustrial Relations as p	provided for by Section 370	0 of the Labor Code, for the
Lineurance carrier and policy	workers' compensation in number are:	surance, as required by Section 370					1
Carrjer		Policy Number			Expiration Dat	te	
Name of Agent					Phone #		
Arcertify that, in the perform that, if I should become subj	ect/to the workers' compe	ch this permit is issued, I shall not en ensation provisions of Section 3700 o	ploy any person i f the Labor Code,	n any manner so I shall forthwith c	as to become subject t comply with those provis	o the workers' compensation ions. pate10-(_4	
DECLADATION DECODIN	IC CONSTRUCTION I EN	DING AGENCY					
I hereby affirm under penalty	of perjury that there is a	construction lending agency for the p	erformance of the	work for which t	his permit is issued (See	ction 3097, Civil Code).	
Lender's Name By my signature below, I cer	tify to each of the followin		r's Address				
I am the property owner	or authorized to act on th	e property owner's behalf.					
I have read this applicat	ion and the information I h	have provided is correct.		ļ			
I agree to comply with a	Il applicable city and cour	ty ordinances and state laws relating	to building constru-	uction.	-	<u> </u>	
I authorize representativ	es of this city or county to	enter the apove identified property f	or inspection purp	Oses. Owner's or Auth	orized Agent's Name	Rev Grad 1	Date 0420
		DECLARATION OF COMPLIANCE WITH					
ACTION	DATE BY U	REGULATIONS PART 61 OF TITLE 40 AN			JSE OINLET		
PERMIT EXPIRED		I SUBNITTED A BESTUS NOT IFICAT	ION TO				
PERMIT CANCELLED		EPA .					
PERMIT EXTENDED						,	
PERMIT FINAL		ASBESTOS NOTIFICATION IS NOT A	PLICABLE TO	1			
CERTIFICATE OF		PROPOSED DEMOLITION					
OCCUPANCY ISSUED		SIGNATURE:		i			



City of Newport Beach Community Development Department - Building Division 100 Civic Center Drive, Newport Beach, CA 92660 Permit Counter Phone: (949) 718-1888 newportbeachca.gov/civic Combination Type -Work Class - New



COMB Permit : **F2021-0383**

9

Plan Check No : 2014-2021 Issued Date : 09/01/2021 Final Date: Permit Status: Issued Inspection Area : 1

PERMITS EXPIRE 180 DAYS AFTER ISSUANCE OR LAST VALID INSPECTION, BUT NO LATER THAN 3 YEARS FROM ORIGINAL ISSUANCE DATE NO CONSTRUCTION RELATED NOISE ON SATURDAY OR SUNDAY IN HIGH DENSITY AREAS AND NO WORK ON SUNDAY AND HOLIDAYS IN ALL AREAS

Job Address: 914 W OCEAN FRONT Description: NEW SFR - FIRE SPRINLERS (24) HEADS ()	Legal Desc : N TR 234 BLK 9 LOT 4 (2019-2085)	
Owner : PAYAM CHARLES ATALL Address : 24881 ALICIA PKWY, G LAGUNA HILLS, CA 92653 Phone : Applicant : Address : Phone :	Contractor : FIREPROOF FIRE PROTECTION Address : 1101 KINGSTON DR. LA HABRA, CA 90631 Phone : (714) 476-5370 Con State Lic : 876004 Lic Expire : 04/30/2026 Bus Lic : BT30040107 Bus Lic Expire : 07/31/2025 Workers' Compensation Insurance Carrier : NATIONAL CASUALTY COMPANY	Architect : Address : Phone : State Lic : Engineer : Address : Phone :
Owner/Builder : Address :	Policy No : WCC336253A W. C. Expire : 2/15/2025	Designer : Address :
Phone :		Phone :
Code Edition : Type of Construction : Occupancy Groups : Bldg Height :	Fire Sprinklers :NOFire Hazard Zone :NONo of Units :0No of Stories :2	Construction Valuation :\$0.00Added/New/TI sq. ft. Bldg :0Alteration sq. ft. Bldg :0Add/New sq. ft. Garage :0TOTAL sq. ft. :0
Building Setbacks :Front: 8, Side: 3, Side: 3, Rear: 0Flood Zone :XUse Zone :R-1 - Single-Unit Residential		
PROCESSED BY :		
SPECIAL CONDITIONS:		

н. С 23					:		
OWNER-BUILDER	R DECLARA	TION					
I hereby affirm under penalty of perjury that I am exempt from the Contractors' State Licens (Section 7031.5, Business and Professions Code: Any city or county that requires a permit to of the permit to file a signed statement that he or she is licensed pursuant to the provisions of the Professions Code) or that he or she is exempt from licensure and the basis for the alleged exe not more than five hundred dollars (\$500).					, improve, demoli State License Lav	ish, or repair any structure, prior to it v (Chapter 9 (commencing with Sect	s issuance, also requires the applicant for tion 7000) of Division 3 of the Business and
Business and Profession	e Code: The C	Contractors' Sta	wages as their sole compensation, will on the License Law does not apply to an own however, the building or improvement is	her of property	who, through em	plovees' or personal effort, builds or	improves the property, provided that the
improved for the purpose	e of sale).				1		
apply to an owner of prop	perty who build	is or improves	cting with licensed Contractors to constru- thereon, and who contracts for the project	ts with a licen:	Section 7044, Bu sed Contractor pu	isiness and Professions Code: The insuant to the Contractors' State Lice	Contractors' State License Law does not ense Law).
I am exempt from lic	ensure under f	the Contractors	' State License Law for the following rea	son:			
sell a structure that I hav	e built as an o	wner-builder if	my personal residence in which I must n it has not been constructed in its entirety s application is submitted or at the follow	by licensed co	ontractors. I under	rstand that a copy of the applicable i	nents covered by this permit, I cannot legally law, Section 7044 of the Business and
Signature of Property Ov	wher or Authori	ized Agent	s appreciation is addimited of at the follow	ing tree sile	up ar te se te se		Date
LICENSED CONTRA	CTOR'S DEC	CLARATION					
I bereby affirm under per	nality of perium	that I am licen	sed under provisions of Chapter 9 (comr	nencing with S	ection 7000) of D _ Date	ivision 3 of the Business and Profes Contractor Signature	sions Code, and my license is in full force
WORKERS' COMPEN	ISATION DE	CLARATION					1
COST OF COMPENSATION, DA	MAGES AS PROV	ADED FOR IN SEC	FION 3706 OF THE LABOR CODE, INTEREST, AND	N EMPLOYER TO ATTORNEY'S FEE	CRIMINAL PENALTIEI S.	S AND CIVIL FINES UP TO ONE HUNDRED T	HOUSAND DOLLARS (\$100,000), IN ADDITION TO THE
I hereby affirm under per							
performance of the work	for which this	permit is issue	d. Policy No.				by Section 3700 of the Labor Code, for the
incurance carrier and not	iev number an	<u>م.</u>					permit is issued. My workers' compensation
Carrier	-		Policy Number			Expiration Date	
Name of Agent					:	Phone #	
L certify that, in the per that, if I should become s	rformance of the subject to the s	he work for whi workers' compe	ch this permit is issued, I shall not emplo ensation provisions of Section 3700 of the	y any person i e Labor Code,	n any manner so I shall forthwith co	as to become subject to the workers omply with those provisions.	s' compensation laws of California, and agree
	-	-					
Signature of Applicant DECLARATION REGAR	DING CONST nalty of perjury	RUCTION LEN	construction lending agency for the perfe	rmance of the	work for which th		
Lender's Name By my signature below, I			Lender's	Address			
By my signature below, I	certify to each	n of the followin	g:	:			
I am the property ow	mer or authoriz	zed to act on th	e property owner's behalf.				
I have read this appli	ication and the	e information I I	nave provided is correct. Ity ordinances and state laws relating to I	uilding constra	uction		
I agree to comply with	in all applicabl	e city and cour aity or courty to	enter the above-identified property for it	spection num	nses.		
Signature of Property Ow			renter the above-documed property for a	Print Property	Owner's or Autho	rized Agent's Name	Date
			DECLARATION OF COMPLIANCE WITH COD	and the second se	FOR OFFICE US		
ACTION	DATE	BY	REGULATION OF COMPLIANCE WITH COL REGULATIONS PART 61 OF TITLE 40 AND A 1403	QMD RULE	FOR OFFICE 0.	SE ONEI	
PERMIT EXPIRED			DI SUBMITTED ASBESTOS NOTIFICATION	то			
PERMIT CANCELLED					1		
PERMIT EXTENDED	·						
PERMIT FINAL			ASBESTOS NOTIFICATION IS NOT APPLI	CABLE TO	1		
CERTIFICATE OF			PROPOSED DEMOLITION	:			
OCCUPANCY ISSUED			SIGNATURE:		<u> </u>		L

.



COMMUNETY DEVELOPMENT DEPARTMENT BUILDING DIVISION 100 Cwie Center Drive | P.O. Box 1758 | Newport Beach, CA 92658-8915 www.newportbeachen.gov | (949) 644-3200

PRE-GRADE MEETING AGREEMENT

JOHN ANDRESS: OCEAN FROM

- 1. The grading plan check number for this site is <u>XZO16-208K</u> and will be referred to in all reports, certifications and correspondence.
- 2. <u>STOP ORDERS</u> Whenever any work is being done contrary to the provisions of the City Codes, the Chief Building Official or his authorized representative may order the work stopped by notice in writing service on any periode eligaded in the doing or causing such work to be done and any such persons shall further the stop such work until authorized by the Chief Building Official to proceed with the work.
- 3. The stamped set of approved plans shall be on the job site at all innes,
- 4. <u>NOTFICATION OF MONCOMPLIANCE</u> II, in the course of fulfilling their responsibilities, the civil angineer, auveyor, the solid angineer, the angineering geologist or the beding agent finds that the work is not being done in conformance with the approved grading plans, the discrepancies shall be reported limitediately in writing to the person in charge of the grading work and to the Sulking Division. Recommendations for corrective measures, if necessary, shall be submitted to the Building Division for approval.
- 5. When import or export of materials is required, hauf routes to and from the site shall be approved by the City Traffic Engineer and hauling procedures shall be in accordance with Chapter 15 of the Newport Reach Manicipal Code (NBMC). Contractor shall use Best Management Practices (BMP's) to lucture that all water quality issues are addressed.
- 6. Between October 1 and April 30, prosion control BMP measures shall be in place. During the remainder of the year day season wind erosion BMP's (dust control) shall be implemented. Sediment control BMP's (shall be installed and mathematical at all operational storm drain fails internal to the project. BMP's to control off-site solution training at all operational storm drain fails internal to the project. BMP's to control off-site storm control and the individual for the storm control off-site storm construction activities shall be implemented. Appropriate BMP's to prove contamination of storm plane from construction activities shall be implemented. A "weather biggered" action plan and the shifty to deploy BMP's to project all exposed portions of the site within 48-hours when the Mallondi Weather Service forecasts a 50% or greater chaine of rain.
- All fills shall be compacted throughout to a minimum of 90 percent compaction as determined by ASTER test method 1557 and approved by the softs angineer. Compaction tests shall be performed according to the preliminary softs report.
- 8. All trench (Including Interior and exterior utility trenches) and retaining wall backfill shall be compacted throughout to a minimum of 90 percent relative compaction and approved by the soils engineer.
- 9. Whenever work on which required inspection/leating is covered by additional work without first being inspected/tested, the Chief Building Official shall require by written notice that the work he exposed for examination. The work of exposing and recovering shall not entail or be subject to expense to the City of Newport Beach and will be the sole expense of the Peimittee.
- 10. Landscaping of all slopes and pads shall be hi accordance with 15, 10, 138 of the MBMC,
- 11. Approved drainage provisions shall be used to protect adjoining properties during the grading operation.

				ling operation is ready for each of the
12.	Th fol	a parmitina os his agant shall nothiy the Building Divisio coving inspections:	to make water by the	next leave than two days before any grading
	2 .	a partners of us total coving inspections: <u>PRE-GRADE MEETING</u> When the partnittee is ready to or brunking is stated.	i Linguis an one of the	ne elevieres cur méters plansmissing av pâpe at
404	b.,	or brunking is stated. <u>DRAINAGE DEVICE INSPECTION</u> After forming of int subdrains, but before any concrude or filter instacted is p	raca draina, dua piacad	(1) 1400 (1999) 1999 (1999) 1999 (1999) 1999 (1999) 1999 (1999) 1999 (1999) 1999 (1999) 1999 (1999) 1999 (1999)
	G.,	THE DESCRIPTION OF AN		
		PORTAL GRADING When all rough grading has been a	in his address and the	nagh grade report shall be provided to Realding Impactor's discretion
	weeker.			the state of the second st
	豢,	russal. When all work, including installation of all deal completed and the securicited plan, professional approx	win and the rect	éraci reștoriu henva benu scharman.
13.	En	Contraction (D), Crustian and Contraction of Annual Contractio of Annual Contraction of		the second days down descent for a second find the second for the
14.	and a	gineer or Engineering Generation with property come on in the start of grading, all permittent property come peoplems, proof of recordation of the "corner record" of		
	per l		······································	are at a manifering franke of the City of
1 .	Th Na	related. a undersigned admoniacige a copy of the above and aquori Reach, the recommendations of the project solis	report and any s	partial requirements of the permit.
16.	Pr	on to foundation inspection a Line and Grade Certific	nins Formi mices: a rad Odrawi visilioti	Repeared and the responsivel.
1-1	A 15	word and antical headness wassed bes parameters a supervision of the programmer of	meeting universe a	Ling of Redshift 1967 A Constant mathematical and the second second second second second second second second s
17.	greger greger	Departure	-	
	Meit	room Rearing Cien Cathrobs	DESIGN CIVIL	WillPolph
Byi	(Alberta	pl augel	By:	7.50 c2 camina Capistrano
Add	Teese	19 12 PO BON 7829 ABCA.	Addition	PH 7-464 - BIT 5
Tele	· · · ·	114-749-0600	Telephones	and an adverse the second second and the second
	7	$\tilde{\rho}$ and ρ ρ . It	GEOLOGIST.:	
	yte;	CHINICAL ENCINEER: 1 McCarthy Cousulty,	Hy:	n pendagatan dari bertan yang dari bertan dari bertan kana bertan dari bertan dari bertan dari bertan dari bert
Byt			Address:	1999 (1999 (1999) (1999) (1999) (1999) (1999) (1999) (1999) (1999) (1994
Adia		1. San an mart S	Telephones	
Tele	il here.			The Connol (Gauga) Controlos
gr/	UØ	O CONTRA J. Parys	COORDINATO: By:	
國的		Dalls 1	Address:	Popet 78-29 Auting Forder
Adai	i qs		Telephone	714-749-6622
Tele	o la:		1	PHONE # 349-694.3262
NEV	(PO	RT BEACH REPRESENTATIVE: Josh Kinde	<u>>_</u> [<u></u>	A A 14-Sec / units of TennetWith Statements
INSI	°EC	TION REQUESTS: (949) 644-3255		
Ho Sa	nici: Euro	<u>rt Beach Construction Houses</u> ny through Friday: 7:00 a.m. to 6:30 p.m. lays: 8:00 a.m. to 6:00 p.m. rk on Sundays and <u>Holidays</u> –		• · · ·
CW #	79 Q	I BY FART IN PURCHASED IN COMPANY AND		

Formskragentin meesking agreemater 8-12

a the second sec

.

.



COMMUNITY DEVELOPMENT DEPARTMENT BUILDING DIVISION 100 Civic Center Drive | P.O. Box 1768 | Newport Beach, CA 926588915 www.newportbeachca.gov | (949) 644-3200

BUILDING FORMS SETBACKS AND TOP OF SLAB/FLOOR ELEVATION CERTIFICATE

The purpose of this certificate is to insure that the structure is located properly on site per the approved drawings. This certificate also verifies the top of slab/floor elevation noted on the approved drawings.

After the top of slab/floor elevation is verified to match the elevation specified on the approved drawings, the contractor and inspector can measure the height of the structure to the top of slab/floor to verify that it is equal or less than the dimension shown on building sections and elevations.

This form must be filled out by a registered surveyor or civil engineer authorized to perform surveys. The survey must be done after the concrete forms are in place or preferable after the concrete slab is poured or raised floor is built, but prior to starting wall framing.

Engineer/Surveyor's Name William D. Rolph, PE, PLS License # 76698 & 9831

Engineer/Surveyor's Address CivilScapes Engineering, Inc. 28052 Camino Capistrano #213, Laguna Niguel

Job Address 914 E Oceanfront Newport Beach

Setbacks: Sketch a site plan and specify surveyed setbacks (use back page).

* Top of slab/floor elevation: 12.50

* If slab/floor elevation varies, sketch a plan or section through slab on the back page and specify the elevations. Use same datum used in the survey of record.

I certify that the setbacks are X, are not \Box , per City approved plans. Describe any deviations from plans:

I certify that top of slab/floor elevation(s) is \square , is not \square , per City approved drawings. Describe any deviations from plans:

12/3/2020


Date

Forms/SetbacksandTopofSlabElevationCert.




Engineer/Surveyor's stamp and signature



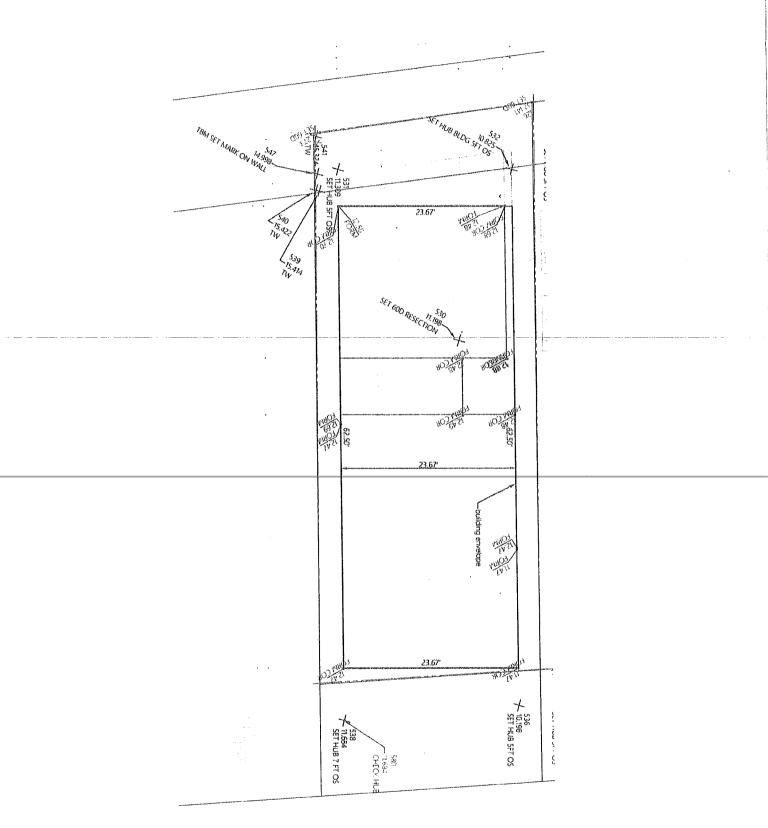

DOCUMENT NUMBER 2020-

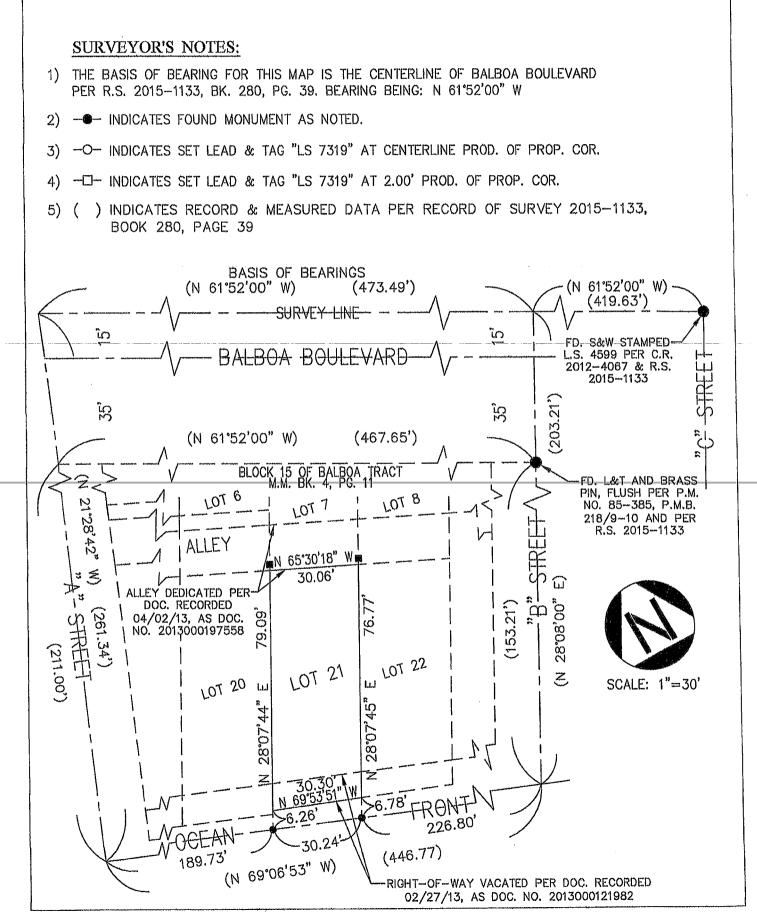



November 30, 2020

Charles Ataii Ocean Property Rentals, LLC 170 Newport Center Drive, Suite 260 Newport Beach, CA 92660 File No: 8262-10 Report No: R3-8262

Subject: Earthwork Observation/Testing Report Residential Construction Lot 22, Block 14, Balboa Tract 914 East Oceanfront Newport Beach, California

Grading Permit No: X2019-2085

References: See attached list

This report presents the results of our observation and testing services performed during the grading of the property located at 914 East Ocean Front on the Balboa Peninsula in Newport Beach, California. The purpose for our geotechnical services was to observe and document the grading operations as part of the development of a graded pad area for the construction of a new residential structure and associated improvements. Based on our observations and review of the test results, it is our opinion that the grading was performed in substantial conformance with the City of Newport Beach and project grading requirements.

PROJECT DATA

<u>Site:</u>	914 East Oceanfront Newport Beach, California
Owner:	Ocean Property Rentals, LLC
General Contractor:	RL Carroll
Grading Contractor:	JD Demo and Grading, Inc.
Civil Engineer:	Civil Scapes, Inc.
Regulatory Agency:	City of Newport Beach
Grading Plans:	Civil Scapes, Inc., 2020, "Precise Grading, 914 East Ocean Front, Newport Beach, California, 1/16/20," Sheet C2
Observation Period:	November 2, 2020, through November 9, 2020

23 Corporate Plaza, Suite 150, Newport Beach, CA 92660 Phone 949 629 2539 | Email info@rmccarthyconsulting.com

SITE LOCATION

The subject property is located on the south side of the Balboa Peninsula. The lot is bordered on the west and east by adjacent residential properties. The property is beyond the eastern terminus of East Oceanfront and the front patio access is via the Newport Balboa Bike Trail/ Boardwalk.

GRADING AND EARTHWORK

A. General

The former site structures, improvements and vegetation were demolished and cleared from the property prior to and during grading. Site conditions were generally as expected based on preliminary exploration as reported in the references. 914 E Oceanfront was graded concurrently with the adjoining lot on the west, 912 E Oceanfront.

B. <u>Preparation of Existing Ground</u>

Within the building pad area, ground preparation consisted of overexcavation of existing earth materials to expose the on-site sands at depths of at least 3 feet below the previous existing site grades within the building pad. On-site exposed materials consisted of dune deposits and marine deposits comprised of tan to gray-brown sand with shell fragments. Incidental, shallow, undocumented fill materials and residual soils, where encountered, were removed as part of the grading within the building areas. Our field geologist and/or engineer observed the removal areas prior to placement of fill. Groundwater was not encountered in the excavations. Excavations thus prepared were determined to be suitable for support of the fill soils.

C. Fill Placement and Compaction

Prior to placement of fill, the exposed surface was scarified, cement-treated, moisture conditioned, and compacted to a minimum of 90 percent relative compaction. Subsequent fill soils were generally placed in 6- to 8-inch loose lifts, brought to near optimum moisture content, cement-treated, and compacted. Test results indicate that a minimum of 90 percent relative compaction, as determined by ASTM D1557, was achieved. The maximum depth of fill placed was on the order of 4 feet.

Fill material included on-site yellow/gray-brown, cement-treated sand with mollusk shell fragments.

Equipment used for compaction included a CAT 287B track loader. Moisture was added using a fire hose.

Based on the results of our field density testing, it is our opinion that a minimum of 90 percent relative compaction was achieved. Density tests were performed in accordance with ASTM: D1556 (Sand Cone Method) and/or ASTM D6938 (Nuclear Gauge Method). Field Density Test Results are tabulated in Table 1, Results of Field Density Tests. The approximate locations of density tests are shown on the Geotechnical Plot Plan, Figure 1.

Representative samples of the site soils used as fill were returned to the laboratory for testing. Laboratory tests for maximum density and optimum moisture content were performed in accordance with ASTM D1557 (the Five Layer Method). The results are presented in Table 2, Laboratory Maximum Dry Density/Optimum Moisture Relationship.

Testing was performed on representative areas to render a professional opinion as to the compaction of fill materials. It is our opinion that sufficient testing was performed to arrive at the conclusions stated herein; however, this is an opinion and is not a warranty that all fill materials are at 90 percent relative compaction.

CONCLUSIONS AND RECOMMENDATIONS

<u>General</u>

Based upon field observations and test results, it is our opinion that grading and compaction described herein was accomplished in accordance with the project requirements and the grading requirements of the City of Newport Beach. Field density testing indicated that a minimum of 90 percent relative compaction was achieved at the locations tested as part of the building pad and site grading.

Based on the observations and testing as described herein, the fill materials placed within the building pads and graded exterior areas at the site are considered suitable for the intended use.

The on-site fill soils have a very low expansion potential.

Foundation and Slab Recommendations

The materials encountered during grading were as anticipated in our Geotechnical Investigation report dated October 31, 2018. The fill materials consist of non-expansive sands. The foundation recommendations provided in the referenced report are, therefore, applicable to the as-graded site.

Conditions were as anticipated in the referenced reports. The foundation recommendations provided in the referenced report (Reference 26, 10-31-2018) are, therefore, applicable to the as-graded site. A slab-on-grade foundation system is planned as indicated on the approved building plans. The near surface materials exhibit a very low expansion potential.

The Contractor should verify that the finished pad grades at an appropriate level for the installation of the sub-slab materials and the 7-inch thick concrete slab.

Concrete Construction Components in Contact with Soil

Various components within concrete that is in contact with soil may be subject to corrosion over time. To help mitigate corrosion in the marine environment, sulfate resistant cement should be used in concrete that may be in contact with on-site soils or ground source water. Attention to maximum water-cement ratio and the minimum compressive strength may also help mitigate deterioration of concrete components. The results of corrosivity tests on the on-site soil are provided in Appendix C of Reference 26.

Type V cement or an appropriate alternate is, therefore, recommended with a maximum watercement ratio of 0.5 percent. The minimum concrete compressive strength should be at least 4,000 pounds per square inch.

It is recommended that a concrete expert be retained to design an appropriate concrete mix to address the structural requirements. In lieu of retaining a concrete expert, it is recommended that the 2019 CBC, Section 1904 and 1905, be utilized which refers to ACI 318. Testing should be performed during grading when fill materials are identified to confirm the sulfate concentration.

Metal Construction Components in Contact with Soil

Metal rebar encased in concrete, iron pipes, copper pipes, lift shafts, air conditioner units, etc., that are in contact with soil or water that permeates the soil should be protected from corrosion that may result from salts contained in the soil. Recommendations to mitigate damage due to corrosive soils, if needed, should be provided by a qualified corrosion specialist. The results of corrosivity tests on the on-site soil are provided in Appendix C of the referenced report.

Foundation Excavations

All excavations should be observed by the Geotechnical Engineer prior to placement of forms, reinforcement, and concrete for verification of conformance with the intention of these recommendations. All excavations should be trimmed neat, level, and square. All loose or sloughed material should be removed prior to the placement of concrete. Materials from footing excavations should not be spread in house slab-on-grade areas unless they are watered and compacted to meet the required minimum density.

Hardscape Design and Construction

Hardscape improvements may utilize conventional foundations in compacted fill. Cracking and offsets at joints are possible; however, occurrence may be minimized by appropriate drainage and the use of thickened edge beams to limit moisture transfer below slabs.

Concrete flatwork should be divided into as nearly square panels as possible. Joints should be provided at maximum 8 feet intervals to give articulation to the concrete panels (shorter spacing is recommended if needed to square the panels).

Landscaping and planters adjacent to concrete flatwork should be designed in such a manner as to direct drainage away from concrete areas to approved outlets. Planters located adjacent to principal foundation elements should be sealed and drained; this is especially important if they are near retaining wall backfills. Flatwork elements should be a minimum 4.5-inches thick (actual) and reinforced with No. 4 bars 18-inches on center both ways. Subgrade soils should be well moistened prior to placement of concrete.

All concrete hardscape subgrade should be observed by our representative immediately prior to placement of reinforcing steel. We recommend that your concrete subcontractor obtain a written approval from our office prior to pouring any concrete that is in contact with soil.

Surface and Subsurface Drainage

1. Finished Grade and Surface Drainage

Finished grades should be designed and constructed so that no water ponds in the vicinity of footings, subterranean walls or slopes. Drainage design in accordance with the 2019 CBC, Section 1804.4, is recommended or per local City requirements. Roof gutters should be provided and outflow directed away from structures in a non-erosive manner as specified by the Project Civil Engineer or Landscape Architect. Proper interception and disposal of on-site surface discharge is presumed to be a matter of civil engineering or landscape architectural design.

2. Drainage and Drainage Devices

The performance of the planned foundation and improvements is dependent upon maintaining adequate surface drainage both during and after construction. The ground surface around foundations and improvements should be graded so that surface water will not collect and pond. The impact of heavy irrigation can artificially create perched water conditions. This may result in seepage conditions where previously none existed.

Sources of uncontrolled water, such as leaky water pipes or drains, should be repaired if identified.

The Owner should be aware of the potential problems that could develop when drainage is altered through construction of retaining walls, paved walkways, utility installations or other various improvements. Ponded water, incorrect drainage, leaky irrigation systems, overwatering or other conditions that could lead to unwanted groundwater infiltration must be avoided.

Area drains should be installed in all planter and landscape areas. Planter surfaces should be sloped away from building areas in accordance with Code requirements. Roof drainage should be tight-lined into the area drain system or carried to outlets away from building foundations.

Utility Trench Backfill

Utility trench backfill should be placed in accordance with Appendix D, Standard Grading Guidelines, contained in the referenced report. It is the Owner's and Contractor's responsibility to inform Subcontractors of these requirements and to notify R McCarthy Consulting, Inc. when backfill placement is to begin. It has been our experience that trench backfill requirements are rigorously enforced by the local agencies.

The on-site soils are suitable for use as trench backfill. Fill materials should be placed at near optimum moisture content and compacted under the observation and testing of the Soil

November 30, 2020	File No: 8262-10
	Report No: R3-8262

Page: 6

Engineer. The minimum dry density required for compacted backfill material is 90 percent of the maximum dry density as determined by ASTM D1557-12.

If utility contractors indicate that it is undesirable to use compaction equipment in close proximity to a buried conduit, we recommend the utilization of lightweight mechanical equipment and/or shading of the conduit with clean granular material, which could be thoroughly jetted in place above the conduit prior to initiating mechanical compaction procedures. Bedding materials should have a sand equivalent not less than 30. Other methods of utility trench compaction may also be appropriate as approved by the Geotechnical Engineer at the time of construction.

The walls of temporary construction trenches are expected to be stable when cut into fill soils, with only minor sloughing, provided the total depth does not exceed about 5 feet. Shoring of excavation walls or flattening of slopes may be required if greater depths are necessary. All work associated with trench shoring must conform to the State of California Safety Code. The depth of the site utilities is unknown at this time. Excavation exceeding 5 feet below site grades should be reviewed by the Geotechnical Consultant to provide recommendations prior to digging.

Trenches should be located so as not to impair the bearing capacity or cause settlement under foundations. As a guide, trenches subparallel to foundations should be clear of a 45-degree plane extending outward and downward from the edge of the foundations.

Construction Considerations

During the grading process and prior to the complete construction of permanent drainage controls, it shall be the responsibility of the Contractor to provide good drainage and prevent ponding of water and damage to adjoining properties, slopes or to finished work on the site. After the Geotechnical Engineer has finished observations of the completed grading, no further excavations and/or filling shall be performed without the approval of the Geotechnical Engineer.

Observation and Testing

Geotechnical observation and testing during construction are required to verify proper removal of unsuitable materials, check that foundation excavations are clean and founded in competent material, to test for proper moisture content and proper degree of compaction of fill, to test and observe placement of wall and trench backfill materials, and to confirm design assumptions. It is noted that the CBC requires continuous verification and testing during placement of fill, pile driving, and pler/caisson drilling.

A R McCarthy Consulting, Inc. representative shall observe the site at intervals appropriate to the phase of construction, as notified by the Contractor, in order to observe the work completed by the Contractor. Such visits and observation are not intended to be an exhaustive check or a detailed inspection of the Contractor's work but rather are to allow R McCarthy Consulting, Inc., as an experienced professional, to become generally familiar with the work in progress and to determine, in general, if the grading and construction is in accordance with the recommendations of this report.

R McCarthy Consulting, Inc. shall not supervise, direct, or control the Contractor's work. R McCarthy Consulting, Inc. shall have no responsibility for the construction means, methods, techniques, sequences, or procedures selected by the Contractor, the Contractor's safety precautions or programs in connection with the work. These rights and responsibilities are solely those of the Contractor.

R McCarthy Consulting, Inc. shall not be responsible for any acts or omission of the Contractor, Subcontractor, any entity performing any portion of the work, or any agents or employees of any of them. R McCarthy Consulting, Inc. does not guarantee the performance of the Contractor and shall not be responsible for the Contractor's failure to perform its work in accordance with the Contract Documents or any applicable law, Codes, rules or regulations.

Construction-phase observations are beyond the scope of this investigation and budget and are conducted on a time and material basis. The responsibility for timely notification of the start of construction and ongoing geotechnically-involved phases of construction is that of the Owner and his Contractor. We request at least 48 hours' notice when such services are required.

List of Guidelines

The Geotechnical Consultant should be notified to observe and test the following activities during grading and construction:

- To observe proper removal of unsuitable materials;
- To observe the bottom of removals for all excavations for the building pad grading, trenching, exterior site improvements, etc.;
- To observe side cut excavations for retaining walls, trenches, etc.;
- To test for proper moisture content and proper degree of compaction of fill;
- To check that foundation excavations are clean and founded in competent material;
- Prior to and after pre-soaking of the slab subgrade soils (if necessary);
- To check the slab subgrade materials prior to placing the gravel, vapor barrier and concrete;
- To check retaining wall subdrain installation when the pipe is exposed and before it is covered by the gravel and fabric; and again after the gravel and fabric have been placed;
- To test and observe placement of wall backfill materials;
- To test and observe placement of trench backfill materials;
- To test and observe hardscape subgrade, including patio, pool deck and sidewalk subgrade materials;
- To observe any other fills or backfills that may be constructed at the site.

It is noted that this list should be used as a guideline. Additional observations and testing may be required per local agency and Code requirements at the time of the actual construction. The 2019 CBC requires continuous verification and testing during placement of fill materials and during pile/caisson drilling.

File No: 8262-10 Report No: R3-8262 Page: 8

LIMITATIONS

Our description of grading operations, as well as observations and testing, has been limited to those grading operations observed between November 2, 2020 and November 9, 2020. This report does not include line and grade survey results. Elevations and locations used in this report are estimated based on field surveys done by others.

The opinions rendered apply to conditions in the subject areas observed by us as of the date of our indicated site visits. We are not responsible for any changes in the conditions that may occur after that date and outside our purview. Our work was provided consistent with and limited to the standard of care applicable to such services, which is that services were consistent with the professional care and skill ordinarily provided by consultants practicing in the same or similar locality under the same or similar circumstances. No other warranty is expressed or implied.

The opportunity to be of service is appreciated. If you have any questions, please call.

Respectfully submitted,

R MCCARTHY CONSULTING, INC.

Robert J. McCarthy, G. E. 2490 Geotechnical Engineer Registration Expires 3-31-22 Date Signed: 12/2/20



Attachments: Table 1 – Results of Field Density Tests Table 2 – Laboratory Maximum Dry Density/Optimum Moisture Relationship Table 3 – Chemical Tests References Figure 1, Geotechnical Plot Plan • .

File No: 8262-10 Report No: R3-8262

Page: 9

Test No.	Test Date	Location	Depth (feet)	Soil Type	Moisture Content (%)	Dry Density (pcf)	Relative Compaction
1*	11/3/20	912 E. Oceanfront	2	3	10.0	107.3	98
2*	11/3/20	914 E. Oceanfront	2	3	11.4	106.3	98
3*	11/3/20	912 E. Oceanfront	1	3	12.3	107.5	99
4*	11/3/20	914 E. Oceanfront	1	3	10.9	105.1	96
5*	11/3/20	912 E. Oceanfront	FSG	3	10.1	103.7	95
6*	11/3/20	914 E. Oceanfront	FSG	3	10.6	104.5	96
7*	11/5/20	914 E. Oceanfront	2	3	6.0	105.9	97
8*	11/5/20	912 E. Oceanfront	2	3	6.6	106.8	98
9*	11/5/20	912 E. Oceanfront	FSG	3	13.2	105.6	97
10*	11/5/20	914 E. Oceanfront	FSG	3	11.2	106.7	98
11*	11/9/20	912 E. Oceanfront	FSG	3	12.2	106.6	98
12*	11/9/20	914 E. Oceanfront	FSG	3	11.6	107.8	99

TABLE 1 - RESULTS OF FIELD DENSITY TESTS

Notes: *indicates Sand Cone Test; all other tests Nuclear Gauge Method Depth indicated is below finished pad grade

FSG = Finished Subgrade FG = Finished Grade

RT = Retest of Failing Test

TABLE 2 – LABORATORY MAXIMUM DRY DENSITY/ OPTIMUM MOISTURE RELATIONSHIP ASTM D1557-12

Soil Type	Description	Optimum Moisture Content (%)	Maximum Dry Density (pcf)
1	Yellow brown Silty SAND	13	101.5
2	Yellow Brown Silty Sand	8.5	105.5
3	Yellow/Gray-Brown Silty SAND (Cement Treated)	15.0	109.0

November 30, 2020

.

File No: 8262-10 Report No: R3-8262

Page: 10

TABLE 3 – CHEMICAL TEST RESULTS

					Min. Resistivity
			Soluble Sulfates	Soluble	(ohm-cm
Test	Soll		(ppm)	Chlorides (ppm)	Saturated)
Location	Туре	pН	ASTM D4327	ASTM D4327	ASTM G187
B-1 @ 0-5'	SP	7.8	34	27	5,200
Building Pad	2		<500		


R McCarthy Consulting, Inc. 23 Corporate Plaza, Suite 150, Newport Beach, CA 92660

REFERENCES

- Sitetech Inc., 2019, "Topographic Map, Precise Grading Plan, Monica Lisa Corporation Duplex, A.P.N. 048-143-20, 912 East Ocean Front, Newport Beach, CA. 92661," dated 9/4/19, Scale: 1" = 10', Sheet 3 of 3.
- AAKO Geotechnical Engineering Consultants, Inc., 1986, "Soils Engineering Investigation for the Proposed Two Unit Condominium and Residential Structure, 922 and 927 E. Ocean Front, Newport Beach, California, Legal Description: Parcel 1 and 2 of Parcel Map No. 85-385, City of Newport Beach, County of Orange, California," Job No. 5649-F1-A6, May 23.
- 3. American Society of Civil Engineers (ASCE), 2019, ASCE 7 Hazard Tool, https://seismicmaps.org/".
- 4. Barrows, A. G., 1974, "A Review of the Geology and Earthquake History of the Newport-Inglewood Structural Zone, Southern California," California Division of Mines and Geology, Special Report 114.
- Building Seismic Safety Council, 2004, National Earthquake Hazards Reduction Program (NEHRP) Recommended Provisions for Seismic Regulations for New Buildings and Other Structures (FEMA 450), 2003 Edition, Part 2: Commentary, Washington D.C.
- 6. California Building Code, 2016 Edition.
- 7. California Division of Mines and Geology, 1998, "Seismic Hazards Zones Map, Newport Beach Quadrangle".
- 8. California Divisions of Mines and Geology, 2008, "Guidelines for Evaluating and Mitigating Seismic Hazards in California," Special Publication 117A.
- 9. Cal/OSHA Title 8 Regulations, 2006.
- 10. City of Newport Beach, 2014, Community Development Department, Building Division, Building Code Policy, "Liquefaction Study Mitigation Measures," revised July 14.
- 11. City of Newport Beach Seismic Safety Element, 2008.
- CivilScapes Engineering, 2018, "Topographic Survey for Ocean Properties Rentals LLC, 914 East Oceanfront, Newport Beach, CA 92661," dated 8/20/18, Scale: 1" = 8', Sheet 1 of 1.
- 13. Department of the Navy, 1982, NAVFAC DM-7.1, Soil Mechanics, Design Manual 7.1, Naval Facilities Engineering Command.
- 14. Duco Engineering, Inc., 2001, "Report of Soils Investigation, Proposed Second Story Addition to the Existing Residence, 814 East Ocean Front, Newport Beach, California," Job No: 01-067, May 11.
- 15. Earthquake Engineering Research Institute (EERI), 2003, "Evaluation of Tsunami Risk to Southern California Coastal Cities," January.
- 16. EGA Consultants, LLC, 2015, "Geotechnical Investigation for Proposed Residential Development Located at 924 East Oceanfront, Newport Beach, California," Project No: IH922.1, December 31.
- 17. EGA Consultants, LLC, 2015, "Geotechnical Investigation for Proposed Residential Development Located at 926 East Oceanfront, Newport Beach, California," Project No: IH923.1, December 30.
- Hart, E. W., and Bryant, W. A., 1997, "Fault-Rupture Hazard Zones in California, Alquist-Priolo Earthquake Fault Zoning Act: California Division of Mines and Geology," Special Publication 42 (Interim Supplements and Revisions 1999, 2003, and 2007).
- 19. Jennings, Charles W., et al., 1994, "Fault Activity Map of California and Adjacent Areas," California Division of Mines and Geology, Geologic Data Map No. 6.

File No: 8262-10 Report No: R3-8262 Page: 12

- Martin, G. R. and Lew, M., 1999, "Recommended Procedures for Implementation of DMG Special Publication 117, Guidelines for Analyzing and Mitigating Liquefaction Hazards in California," Southern California Earthquake Center (SCEC), University of Southern California, 63 pages, March.
- 21. Morton and Miller, 1981, Geologic Map of Orange County, CDMG Bulletin 204.
- 22. Morton, P. K., Miller, R. V., and Evans, J. R., 1976, "Environmental Geology of Orange County, California: California Division of Mines and Geology," Open File Report 79-8 LA.
- Morton, D. M., Bovard, Kelly H., and Alvarez, Rachel M., 2004, "Preliminary Digital Geological Map of the 30' X 60' Santa Ana Quadrangle, Southern California," Version 2.0, Open-File Report 99-172, Version 2.0 – 2004.
- 24. Morton, Douglas M., and Miller, Fred K., Compilers, 2006, "Geologic Map of the San Bernardino and Santa Ana 30' X 60' Quadrangles, California," U. S. Geological Survey Open File Report 2006-1217.
- 25. Petersen, M. D., Bryant, W. A., Cramer, C. H., Cao, T., Reichle, M. S., Frankel, A. D., Lienkaemper, J. J., McCrory, P. A., and Schwartz, D. P., 1996, "Probabilistic Seismic Hazard Assessment for the State of California," Department of Conservation, Division of Mines and Geology, DMG Open-File Report 96-08, USGS Open File Report 96-706.
- 26. R McCarthy Consulting, Inc, 2018, "Geotechnical Investigation, Proposed Residential Construction, 914 East Oceanfront, Newport Beach, California," File No: 8262-00, Report No: 20180731-1, October 31.
- R McCarthy Consulting, Inc, 2020, "Geotechnical Investigation, Proposed Residential Construction, 912 East Oceanfront, Newport Beach, California," File No: 8366-00, Report No: R1-8366r (Updated CBC), March 19.
- 28. R McCarthy Consulting, Inc, 2020, "Response to 1st City Review, Proposed Residential Construction, 912 East Oceanfront, Newport Beach, California," File No: 8366-00, Report No: R2-8366, May 6.
- Schmertmann, Dr. John H., 1977, "Guidelines for CPT Performance and Design," prepared for the Federal Highway Administration, U. S. Department of Transportation, FHWA-TS-78-209, February.
- Seed, Bolton H. and Idriss, I. M., 1974, "A Simplified Procedure for Evaluating Soil Liquefaction Potential," Journal of Soil Mechanics, ASCE, Vol. 97, No. SM9, September, pp. 1249-1273.
- 31. Structural Engineers Association of California (SEAOC), 2019, OSHPD Seismic Design Maps, https://seismicmaps.org/".
- 32. Tan, Siang, S., and Edgington, William J., 1976, "Geology and Engineering Geology of the Laguna Beach Quadrangle, Orange County, California," California Division of Mines and Geology, Special Report 127.
- 33. Terzaghi, Karl, Peck, Ralph B., and Mesri, Ghoamreza, 1996, "Soil Mechanics in Engineering Practice, Third Edition," John Wiley & Sons, Inc.
- 34. Tokimatsu, K., and Seed, H. B., 1987, "Evaluation of Settlements in Sands Due to Earthquake Shaking," Journal of Geotechnical Engineering, ASCE, Vol. 113, No. 8, pp. 861-878.
- 35. Vedder, J. G., Yerkes, R. F., and Schoellhamer, J. E., 1957, Geologic Map of the San Joaquin Hills-San Juan Capistrano Area, Orange County, California, U. S. Geological Survey, Oil and Gas Investigations Map OM-193.
- Zhang, G., Robertson, P. K., and Brachman, R. W. I., 2002, "Estimating Liquefactioninduced Ground Settlements from CPT for Level Ground," Canadian Geotechnical Journal 39: 1168-1180.

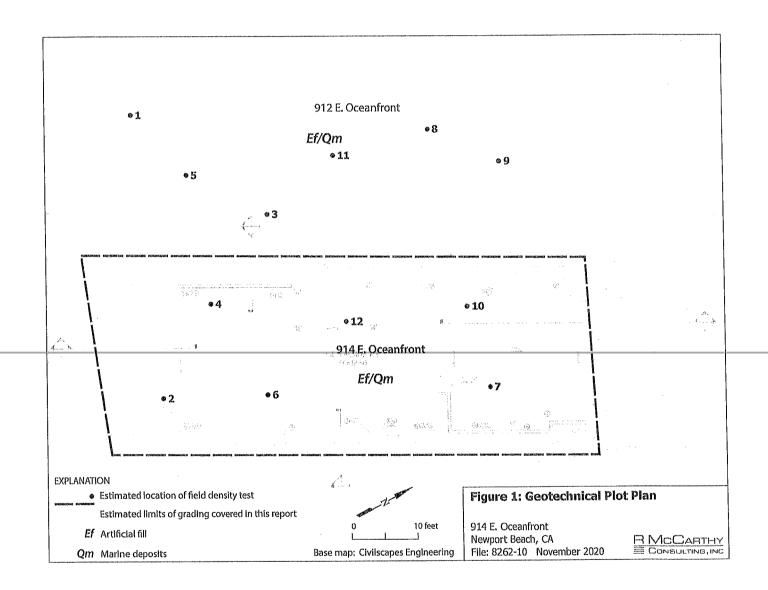



Field Memorandum

Client: Charles Atali

Date: February 4, 2021

Contractor: RL Carroll Construction

File No. 8262-10

Project Address: 914 E. Oceant Front, Newport Beach, CA

Subject: Site observation trench backfill and pad subgrade (GP#X2019-2085)

Arrived on site this morning to test and observe the interior plumbing trench backfill and the slab subgrade for the proposed residence and garage at the request of the general contractor. The interior plumbing trenches had been backfilled prior to my arrival on site. The depths of the plumbing trenches varied in depth between 6 to 12 inches. The contractor was in the process of flattening and compacting the surface soils across the slab subgrade area by means of a vibratory plate compactor. The soils were probed and observed to be dense and moist.

Based on our observation, it is our opinion that, from a geotechnical standpoint, the interior plumbing trenches and pad subgrade were prepared in general compliance with the recommendations of this firm and are considered suitable for the placement of the slab underlayment, steel reinforcement and concrete.

Respectfully Submitted,

R McCarthy Consulting, Inc.

Stephan Cousineau, Staff Engineer

Atophan P. Caurinean



COMMUNITY DEVELOPMENT DEPARTMENT BUILDING DIVISION 100 Civic Center Drive | P.O. Box 1768 | Newport Beach, CA 92658-8915 www.newportbeachca.gov | (949) 644-3200

Structural Observation Report

.

No: 4

Project Address				
911 E Dear T. I	Report Date:	CNB inspector Name:	CNB Permit #:	
Project Address: 914 E. Ocean Front	1-21-22	• • •	X2019-2085	
Dunuing Owner Name:			CNB Plan Check #	
Charles Atai	Same		1519-2019	
Full Name of Structural Observer (SO):	SO E-mail Address:	10 - A 100 - A 10	SO License / Reg. #:	
ALI REZAEI	alierce-eng.com	949-466-9394	C4106B	
		· · · · · · · · · · · · · · · · · · ·		

PLEASE INDICATE STRUCTURAL ELEMENTS AND CONNECTIONS OBSERVED (check applicable boxes)

	FOUNDATIONS	SHEAR WALLS	FRÀMES	DIAPHRAGMS (Floor/Roof)	INDICATE LOCATION(S) OBSERVED	DATE
	Conventional Footings & Slab		Steel		VOGERVED	OBSERVED
	Mat Foundation, Prestressed Concrete	D Masonry		Steel Deck	***************************************	
New Y	□ Calssons, Piles, Grade Beams	☐ Wood or Manuf. Shear Panels	🖾 Masonry	U Wood	NANANA MANANA MANA A MA	······································
	Ci Other:	D Other:	C Other:	🖾 Other:		· ·
		BOVE ARE APPROVED	AND WITHOUT DEP			
		Encies and commen	rs: 🔀			
	Dogervi	ed upon Com	oletion of 1	Zouih MEP		
				- and M when I	<u>, , , , , , , , , , , , , , , , , , , </u>	
					·	
	EINAL STRUCTURA		.41			ACHED PAGES.
	The structure generally	L OBSERVATION REPO	DRT: Foved construction (doormoode and all al	served deficiencies were corr	
ſ				-	served denciencies were com	<u>≱cted.</u>
	i declare that the followin	ig statements are true to	the best of my knowle	edge:	· ·	
	1. I am the licensed	design professional reta	lined by the owner t	o be in responsible	PROPESSION	
ł	2. I, or another license	d design professional wh	om I have declarator	d above and in under	AS AL REAL	iel
	construction stage	to verify that the struct			3 No. 41068	
		on documents; deficiencies which I hav			Exp: 3/31/2/	
-	final acceptance of Division	the structural systems	by the City of Newp	ort Beach, Building	CIVIL	
				11	OF CALIFOR	
	SIGNATURE OF STRUCT	en	• • •	1/21/22	STAMP OF STRUCTURAL O	
L	STRUCTURAL ORSERVATI	RAL OBSERVER OF RECO	D. D.	ATE .		T

STRUCTURAL OBSERVATION DOES NOT WAIVE ANY REQUIREMENTS FOR BUILDING INSPECTION BY AUTHORIZED EMPLOYEES OF THE CITY OF NEWPORT BEACH.

30



COMMUNITY DEVELOPMENT DEPARTMENT BUILDING DIVISION 100 Civic Center Drive | P.O. Box 1768 | Newport Beach, CA 92658-8915

www.newportbeachca.gov | (949) 644-3200

Structural Observation Report

Project Address: 914 E. Ocean Front	Report Date: 5/10 / 21		CNB Permit #: X 2019 - 2085
Sharles Atai	Owner's Mailing Address (if different from site); Same	Owner's Telephone #:	CNB Plan Check# 1519-2019
Full Name of Structural Observer (SO): ALI REZAEI	so E-mail Address: All CrCe-Eng-Com	SO Telephone #:	SO License / Reg. #: C-4-1068

PLEASE INDICATE STRUCTURAL ELEMENTS AND CONNECTIONS OBSERVED (check applicable boxes)

FOUNDATIONS	Shear Walls	FRAMES	(Floor (Floor (Rost))	INDICATE LOCATION(S) OBSERVED	DATE
Conventional Footings & Slab	Concrete	CI Steel	Concrete		an a
D Mat Foundation, Prestressed Concrete	CI Masonry		CI Steel Deck		
Calssons, Piles, Grade Beams	CI Wood or Manuf. Shear Panels	🖾 Masonry	Al Wood	3rd Flr. SHT'cy,	5/10/21
El Other:	디 Other:	CI Other:	El Other:	Contraction of the second s	

ACTEMS CHECKED ABOVE ARE APPROVED AND WITHOUT DEFICIENCIES.

OBSERVED DEFICIENCIES AND COMMENTS

No. 41068 Exp: 3/31/ 23

CI REPORT CONTINUED ON ATTACHED PAGES.

CI FINAL STRUCTURAL OBSERVATION REPORT: The structure generally complies with the approved construction documents, and all observed deficiencies were corrected.


I declare that the following statements are true to the best of my knowledge:

- 1. I am the licensed design professional retained by the owner to be in responsible charge of the structural observation;
- 2. I, or another licensed design professional whom I have designated above and is under my responsible charge, have performed the required site visits at each significant construction stage to verify that the structure is in general conformance with the approved construction documents; 3.

I understand that all deficiencies which I have documented must be corrected, prior to final acceptance of the structural systems by the City of Newport Beach, Building Division.

ER OF RECORD

۰.



STRUCTURAL OBSERVATION DOES NOT WAIVE ANY REQUIREMENTS FOR BUILDING INSPECTION BY AUTHORIZED EMPLOYEES OF THE CITY OF NEWPORT BEACH. Forms\StructuralObservationIteport&Instructions



COMMUNITY DEVELOPMENT DEPARTMENT BUILDING DIVISION 100 Civic Center Drive | P.O. Box 1768 | Newport Blaach, CA 92658-8915 www.newportbeachca.gov | (949) 644-3200

Structural Observation Report

「「「「「「「」」

Projact Address:	Report Date:	CNB Inspector Name:	CNB Permit #: X 2019 - 2085
	Owner's Mailing Address (if different from alb);	Owner's Telephone #:	CNB Plan Check # 1619 - 2019
Charles Atal Full Name of Shuctural Observer (SO): ALI REZAE I	**************************************		SO License / Reg. #: C-41068

PLEASE INDICATE STRUCTURAL ELEMENTS AND CONNECTIONS OBSERVED (check applicable boxes

FOUNDATIONS	SHEAR WALLS	FRAMES	(Floor/Roof)	INDICATE LOCATION(S) OBSERVED	OBSERVED
Conventional Footings & Slab		🖸 Steel	CI Concrete	and the second	1999 1999 1999 1999 1999 1999 1999 199
D Mat Foundation, Prestressed Concrete	C. Masonry	[] Concrete	CI Steel Deck		a fen fin follafin an formalitation of the state of the
☐ Calssons, Piles, Grade Beams	X Wood or Manuf. Shear Panels	CI Masonry	」與 Wood	18+ plr. 3/W +	30.11
C] Other:	Diher:	D Other:	Cl Other:	2 Mper. Shfg.	3.2
RI-	Language and the second sec	A STATUTE OF THE OWNER AND A STATUTE OWN		10 °	

DRITEMS CHECKED ABOVE ARE APPROVED AND WITHOUT DEFICIENCIES.

٩÷

U OBSERVED DEFICIENCIES AND COMMENTS

LI REPORT CONTINUED ON ATTACHED PAGES.

FINAL STRUCTURAL OBSERVATION REPORT:

OTURAL OF

3.

División.

SIGNATURE

The structure generally complies with the approved construction documents, and all observed deficiencies were corrected

I declare that the following statements are true to the best of my knowledge:

- 1. 2.
- I am the licensed design professional retained by the owner to be in responsible charge of the structural observation; I, or another licensed design professional whom I have designated above and is under my responsible charge, have performed the required site visits at each significant construction stage to verify that the structure is in general conformance with the approved construction documents; I understand that all deficiencies which I have documented must be corrected, prior to final acceptance of the structure is the city of Newyort Beerth Building No. 41068 Exp: 9/81/ 23 final acceptance of the structural systems by the City of Newport Beach, Building OF OAL 3-20.2.1 STAMP OF STRUCTURAL OBSERVER DATI

STRUCTURAL OBSERVATION DOES NOT WAIVE ANY REQUIREMENTS FOR BUILDING INSPECTION BY AUTHORIZED EMPLOYEES OF THE CITY OF NEWPORT BEACH. FormalSupplurelightervisionReport & Instructional

32

1.12

• •			•	•	,
SWPAN.		· · ·			
(CATA)	CIT	Y OF NE	WPORT BE	CACH	••
	-	BUILDI	OPMENT DEPA		
	100 Civic Center I <u>Wy</u>	Drive P.O. Box ww.newportbeac	1768 Newport Beau 1ca.gov (949) 644-3	ch, CA 92658-8915 3200	
personal contraction of the second	Stru	ctural Ob	servation R	eport	No. 3
Project Address; 914 Building Owner Name:	E. Ocean Fron.		2-8-21	CNB Inspector Name:	ONB Permit #: X 2019 - 208
Full Name of Structural O	tai	5	dress (if different from site); Anne	Owner's Telephone #:	CNB Plan Check #: 1519 - 2019
ALI REZAE	oserver (SO): E 1	SO E-mail Address:	- E119 . Com	80 Telephone #: 949 - 466 - 9394	SO License / Reg. #: C41068
PLEASE IND	ICATE STRUCTURAL	ELEMENTS AND	CONNECTIONS OB	SERVED (check applic	able boxes)
FOUNDATIONS	SHEAR WALLS	FRÀMES	DIAPHRAGMS (Floor/Roof)	INDICATE LOCATION OBSERVED	(S) DATE OBSERVED
Footings'& Slab	/ □ Concreta □ Masonry	C Steel	Concrete	clabs on Carino	le 2-8-21
Prestressed Concrete □ Calssons, Piles,	U Wood or Manuf.	CI Masonry			
Grade Beams	Shear Panels	D Other:	Ci Other:	4 - 14-16 - 16 - 16 - 17 - 18 - 18 - 19 - 19 - 19 - 19 - 19 - 19	anna an
ITEMS CHECKED	ABOVE ARE APPROVED	AND WITHOUT D	EFICIENCIES.	**************************************	
	IENCIES AND COMMEN	<u>178:</u>	and the second		9
a Martin pipersky a star a speciarly to (Arry Jack -)	and a second	Network and a state of the stat			
and a state of the	and the second	ى مەربىلە بەر مەربىلەر بار بار ئىلغانىيە بەر بەر بار بار بەر بەر بەر بەر بەر بەر بەر بەر بەر بە	• • •	• •	
		an fan yn fan gelan yw en en werg en en an fan fan gelan gelan gener.	1		
CI FINAL STRUCTUR	AL OBSERVATION REP	ORT:	1970)1979-1971-1971-1971-1971-1971-1971-1971	C REPORT CONTINUED O	ا مەركىيە ئىلەر ئىلەر ئىلەر ئىلەر ئىلەر ئىلەر بىلەر بى يەركىيە ئىلەر بىلەر ئىلەر بىلەر بى
	and the state of the		•	oserved deficiencies were	oorrected.
 I am the licensed charge of the struct charge of the struct I, or another license my responsible ch construction stage approved construct I understand that a 	ad design professional wi arge, have performed the to verify that the struct	ained by the owner hom I have designat he required site vis ture is in general ve desumented mus	to be in responsible and above and is under its at each significant conformance with the	No. 410 Exp: 3/3 Month Exp: 3/3 STAMP OF STRUCTU	1/21



COMMUNITY DEVELOPMENT DEPARTMENT BUILDING DIVISION

100 Civic Center Drive | P.O. Box 1768 | Newport Beach, CA 92658-8915 www.newportbeachca.gov | (949) 644-3200

Structural Observation Report

No: 2

	Project Address	and the state of the second			
	Project Address: 914 E. Ocean From	Report Date:	CNB Inspector Name:	CNB Permit #:	
J	- 914 E. Ocean Front	1-30-21			
	Building Owner Name:			X2019-2085	
ĺ		Owner's Mailing Address (If different from site);	Owner's Telephone #:	CNB Plan Check #	
	Charles Atai	Same			
- 1	Full Name of Structural Observer (SO):		مريد مريد مريد مريد مريد مريد مريد مريد	1519-2019	
	A & B For Manage of the	SO E-mail Address:	SO Telephone #;	SO License / Reg. #:	
	ALI REZAEI	allerce-eng.com	949-466-9394		
		ST S	1-1-1-444-1314	C41068	

PLEASE INDICATE STRUCTURAL ELEMENTS AND CONNECTIONS OBSERVED (check applicable boxes)

FOUNDATIONS	SHEAR WALLS	FRÀMES	DIAPHRAGMS (Floor/Root)	INDICATE LOCATION(S) OBSERVED	DATE		
Conventional Footings & Slab	Concrete	D Steel	D Concrete	Cout Fla Lake	0856RVED		
Mat Foundation, Prestressed Concrete	디 Masonry	C Concrete	CI Steel Deck	General Contractions			
Calasons, Plles, Grade Beams	Wood or Manuf, Shear Panels	🖾 Masonry	C) Wood	ar yn arwyn ywr yn			
U Other:	C Other:	Other:	Cl Other:		animetyling between surgery - space program for		
ITEMS CHECKED A	ITEMS CHECKED ABOVE ARE APPROVED AND WITHOUT DEFICIENCIES.						
	encies and commen	ITS: /	V	in an			
		and the first of the second		9999 - 1999 - 1999 - 1999 - 1999 - 1999 - 1999 - 1999 - 1999 - 1999 - 1999 - 1999 - 1999 - 1999 - 1999 - 1999 -			
	and the second se	and the second		an ang san ang ang san	ad an an (1 and 1 a 1 an an y an (1 a 1 a 1 a 1 a 1 a 1 a 1 a 1 a 1 a 1		
	LI REPORT CONTINUED ON ATTACHED PAGES.						
FINAL STRUCTURAL OBSERVATION REPORT: The structure generally complies with the approved construction documents, and all observed deficiencies were corrected.							
				oserved deficiencies were corr	ected.		
I declare that the following statements are true to the best of my knowledge:							
1. I am the licensed design professional retained by the owner to be in responsible charge of the structural observation;							
2. I, or another license	2. I, of another ligensed design professional where there design and have a start and have a						
construction stage	construction stars to verify that the table of required site visits at each significant						
final acceptance of Division.	the structural systems	by the City of New	port Beach, Building	la para	X		
				S OF CALLEO	D.		
- Ali lla	2-12-2	· · ·	Ilapini		£2.		
SIGNATURE OF STRUCTU			DATE	STAMP OF STRUCTURAL O	BSÉRVER		
STRUCTURAL OBSERVATI	ON DOES NOT WAIVE ANY DEC	ا در سر دیدگذیند. با منظر این میشود و میرو و میرو و میرو از این م			Contraction of the local division of the loc		

STRUCTURAL DESERVATION DOES NOT WAIVE ANY REQUIREMENTS FOR BUILDING INSPECTION BY AUTHORIZED EMPLOYEES OF THE GITY OF NEWPORT BEACH.



COMMUNITY DEVELOPMENT DEPARTMENT BUILDING DIVISION

100 Civic Center Drive | P.O. Box 1768 | Newport Beach, CA 92658-8915 www.newportbeachca.gov | (949) 644-3200

FIRE SPRINKLER NFPA 13D SYSTEM ROUGH INSPECTION CHECKLIST

	די היי העשר ליין היא שלא שלא שלא שלא שלא שלא שלא האדיר היא האדיר היא של שלא האבע שעיים ליין ביי היא שלא אייר יי היא האדיר שלא היא האדיר היא האדיר האדיר היא האדיר היא האדיר האדיר האדיר האדיר האדיר האדיר האדיר האדיר האדיר האד האדיר האדיר האד	YES	NO	e to a sign of
1.	Riser Construction and Location Aporoval		· · · · · · · · · · · · · · · · · · ·	
	a. Drain valve	-0/		
	b. Backflow device (single check)			
	c. Bell activation device	R		
	d. Inspector's test valve	2		
	e. Riser sized per approved plans			
2	Pressure Test			
	a. System tested at operating pressure for 2 hours	D		
	b. Pressure gauge installed			
3.	Sprinkler Heads shall not be installed in the fillings prior to the fillings			
	being cemented in place (temporary test plugs)			Contraction of the state free of
•	a. Installation and spacing of temporary test plugs		\Box	
4	Pierce	1		
	a. Material installed per plan	I		
	b. Hangers per codes/prevent upward movement			
	c. All CPVC piping shall be installed by persons who have been certified by the manufacturer for installation of CPVC piping			
	d. Piping protected from damage			
5.	Bel		, ⁷ 2	
	a. Wiring installed per code			
	b. Boxes installed at proper locations			
NOTE	CPVC plastic pipe in the garage shall not be exposed. Sprinklers that a	re listed as "(Drick	n ye ye awar yê statî
	= or to plane pipe in the gradye shall be expected. Optimized when a set of "Residential" must be used.			
				<u>x</u>
CORF	ECTIONS AND NOTES:			_

FIRE SPRINKLER NFPA 13D SYSTEM ROUGH INSPECTION APPROVED:				
BY: Dom	R	PERMIT # F2021 - 0383 DATE: 3-31-22		


Attachment No. 2

Three-Year Construction Limit Notice Activities



PERMIT ACTIVITY REPORT (X2019-2085) FOR CITY OF NEWPORT BEACH

Created Date	Activity Type	Activity Name	Activity Number	Activity Comments	Created By
01/10/2025					
	Generic Activity	HEARING APPLICATION SUBMITTED	ACT-000149-2025	HEARING APPLICATION SUBMITTED ON 01-08-2025; ROUTED TO CITY CLERK AND FINANCE ON 01-10-2025.	Tonee Thai
01/02/2025					
	Generic Activity		ACT-000002-2025	Morning Jason, I hope you had a great Christmas and New Year. We have completed the application over your holiday break. I won't be back in town until Friday afternoon. I'll most likely handle this Monday. Thank you, Ron On Thu, Jan 2, 2025, 7:44 AM Rudenick, Jason <jrudenick@newportbeach ca.gov> wrote: Hi Ron Happy New Year! Hope you had a nice Holiday! When you get a second let me know where you are at with the application? Thank you Jason</jrudenick@newportbeach 	Jason Rudenick



Created Date	Activity Type	Activity Name	Activity Number	Activity Comments	Created By
	Email		ACT-000003-2025	Morning Jason, I hope you had a great Christmas and New Year. We have completed the application over your holiday break. I won't be back in town until Friday afternoon. I'll most likely handle this Monday. Thank you, Ron On Thu, Jan 2, 2025, 7:44 AM Rudenick, Jason <jrudenick@newportbeach ca.gov> wrote: Hi Ron Happy New Year! Hope you had a nice Holiday! When you get a second let me know where you are at with the application?</jrudenick@newportbeach 	Jason Rudenick
				Thank you	
				Jason	
01/08/2025					
	Generic Activity	Hearing Application received	ACT-000119-2025	Application received and paid, on SL's desk.	Jason Rudenick
	Generic Activity	Application received	ACT-000118-2025	Application received and paid, on SL's desk	Jason Rudenick
10/14/2024					
	Generic Activity	Stop Work	ACT-004003-2024	Jason to delivery Stop Work Ron Carroll (GC) is aware and is working on next steps. Communications and email have been documented and entered.	Jason Rudenick

10/09/2024

Created Date	Activity Type	Activity Name	Activity Number	Activity Comments	Created By
	Generic Activity	Email	ACT-003932-2024	Email to GC; Good morning Ron	Jason Rudenick
				Received the Fire Sprinkler permit, thank you. It has a small list of corrections for Monty; 1. Revise plans to show added and moved heads throughout house 2. Bell and flow switch to be functional for inspection 3. Revise plan to show underground from meter to riser as inch and a quarter pipe and show new riser location in garage 4. Revise permit to reflect correct address as 914 E. Ocean front It appears we will have to complete the 3yr Hearing application process. Please	
				see attached 3yr Hearing App. This will buy you the time you need for the remaining items.	
				As soon as possible please come down to NB Bay D to drop off the application. -Provide a simple letter	
				stating the Elevator is the remaining item and a couple miscellaneous. -Provide a signed letter from owner stating you /GC can	
				sign and represent. -Pay fee. -Susan will date stamp. -At that time, the application will be processed for review.	
				-Once approved a Hearing date will be provided.	
				We can chat more about the process.	
				Thank you	
				Jason	
				Jason Rudenick Senior Building Inspector Community Development	

100 Civic Center Drive Newport Beach, CA 92660

Created Date Activity Type **Activity Name**

Activity Number Activity Comments

Created By

11/19/2024

Created Date	Activity Type	Activity Name	Activity Number	Activity Comments	Created By
reated Date	Activity Type Email		ACT-004478-2024	 From: Ron Carroll <rl><rl><rl><rl></rl> <!--</td--><td>Created By Jason Rudenick</td></rl></rl></rl>	Created By Jason Rudenick
				 Provide a signed letter from owner stating you /GC can sign and represent. 	
				-Pay fee. -Susan will date stamp. -At that time, the application will be processed for review.	
				-Once approved a Hearing date will be provided.	

Required items for C of O;

reated Date	Activity Type	Activity Name	Activity Number	Activity Comments	Created By
				Permits needed to schedule	
				for Final;	
				-X2019-2085 Main House	
				(with Holds as stated below) -H2021-0538 AC Units (with	
				noise analysis and HERS	
				Cheers)	
				-BBQ /Fire Pit Permit	
				(Required) -Wall Permit (with neighbor	
				agreement)	
				-F2021-0983 Fire Sprinkler	
				Corrections for Monty;	
				1. Revise plans to show	
				added and moved heads throughout house	
				2. Bell and flow switch to be	
				functional for inspection	
				3. Revise plan to show	
				underground from meter to	
				riser as inch and a quarter pipe and show new riser	
				location in garage	
				4. Revise permit to reflect	
				correct address as 914 E.	
				Ocean front	
				Final docs needed for file;	
				-Corner Record (with County	
				Stamp) -Height Cert (need to	
				reference parapets and	
				guards)	
				-Final Grade Report	
				-Final Civil Cert (NB City form) -Final Elevator Cert	
				-CalGreen (NB City Form, see	
				attached)	
				-Plumb Self Cert (NB City	
				Form, see attached) -HERS	
				Holds to remove prior to final; -Public Works; Permit	
				N2020-0645 (just be certain	
				all is good with pw).	
				-Revenue Dept; Hold on final	
				for business license sub	
				contractors list to be submitted to Revenue.	
				Thank you	
				Jason	
				Jason Rudenick Community Development	
				Department	
				Senior Building Inspector jrudenick@newportbeachca.	

gov

	PERMIT ACTIVITY REPORT (X2019-2085)							
Created Date	Activity Type	Activity Name	Activity Number	Activity Comments	Created By			
				949-644-3262 CITY OF NEWPORT BEACH 100 Civic Center Drive, First Floor Bay D, Newport Beach, California 92660 newportbeachca.gov				

Created Date	Activity Type	Activity Name	Activity Number	Activity Comments	Created By
Created Date	Activity Type Generic Activity	email	ACT-004479-2024	Activity CommentsFrom: Ron Carroll <rl><rl><rl><rl><rl><rl><rl><rl><td< td=""><td>Created By Jason Rudenick</td></td<></rl></rl></rl></rl></rl></rl></rl></rl>	Created By Jason Rudenick
				stating the Elevator is the remaining item and a couple miscellaneous. -Provide a signed letter from owner stating you /GC can sign and represent.	
				-Pay fee. -Susan will date stamp. -At that time, the application will be processed for review. -Once approved a Hearing	

Required items for C of O;


Created Date	Activity Type	Activity Name	Activity Number	Activity Comments	Created By
				Permits needed to schedule	
				for Final;	
				-X2019-2085 Main House	
				(with Holds as stated below)	
				-H2021-0538 AC Units (with noise analysis and HERS	
				Cheers)	
				-BBQ /Fire Pit Permit	
				(Required)	
				-Wall Permit (with neighbor	
				agreement)	
				-F2021-0983 Fire Sprinkler Corrections for Monty;	
				1. Revise plans to show	
				added and moved heads	
				throughout house	
				2. Bell and flow switch to be	
				functional for inspection	
				3. Revise plan to show	
				underground from meter to	
				riser as inch and a quarter pipe and show new riser	
				location in garage	
				4. Revise permit to reflect	
				correct address as 914 E.	
				Ocean front	
				Final docs needed for file;	
				-Corner Record (with County	
				Stamp) -Height Cert (need to	
				reference parapets and	
				guards)	
				-Final Grade Report	
				-Final Civil Cert (NB City form)	
				-Final Elevator Cert	
				-CalGreen (NB City Form, see attached)	
				-Plumb Self Cert (NB City	
				Form, see attached)	
				-HERS	
				Holds to remove prior to final;	
				-Public Works; Permit	
				N2020-0645 (just be certain	
				all is good with pw). -Revenue Dept; Hold on final	
				for business license sub	
				contractors list to be	
				submitted to Revenue.	
				Thank you	
				Jason	
				Jason Rudenick	
				Community Development	
				Department	
				Senior Building Inspector	
				jrudenick@newportbeachca.	

gov

created Date	Activity Type	Activity Name	Activity Number	Activity Comments	Created By
				949-644-3262	
				CITY OF NEWPORT BEACH 100 Civic Center Drive, First Floor Bay D, Newport Beach, California 92660 newportbeachca.gov	
1/02/2023					
	Generic Activity	3-YEAR DEADLINE EXTENSION	ACT-002566-2023	MAILED & EMAILED APPROVED 3-YEAR CONSTRUCTION LIMIT EXTENSION TO PROPERTY OWNER	Debi Schank
2/12/2024					
	Email		ACT-004866-2024	Good morning Jason, I'm sorry this hasn't been done yet. The owner of 914 E. Oceanfront has put me in a situation that I've never been involved in. He is in a battle with Public Works over the alley. He's blaming a large portion of the delays on the alley. Which is only a small portion of the delays. Regardless, there's a meeting 12/11 with all of the Public Works king pins including Mike Sinacorie. Oh joy! For 30 plus years I've managed to keep my nose clean with the City of Newport Beach. This isn't sitting well with me! Thanks, Ron	Jason Rudenick

12/05/2024

Created Date	Activity Type	Activity Name	Activity Number	Activity Comments	Created By
	Generic Activity	email	ACT-004698-2024	From GC Ron; Good morning Jason, I'm sorry this hasn't been done yet. The owner of 914 E. Oceanfront has put me in a situation that I've never been involved in. He is in a battle with Public Works over the alley. He's blaming a large portion of the delays on the alley. Which is only a small portion of the delays. Regardless, there's a meeting 12/11 with all of the Public Works king pins including Mike Sinacorie. Oh joy! For 30 plus years I've managed to keep my nose clean with the City of Newport Beach. This isn't sitting well with me!	Jason Rudenick
03/20/2024					
	Generic Activity	Зуг	ACT-001242-2024	Morning Jason, The city of NB hired me to remove, relocate and replace the 6" water main. We finally poured the new alley yesterday. The city says we can't drive on it for two weeks. Nothing has been done for weeks. I'll let ya know the schedule moving forward. Thanks, Ron	Jason Rudenick
	Email	Зуг	ACT-001241-2024	Morning Jason, The city of NB hired me to remove, relocate and replace the 6" water main. We finally poured the new alley yesterday. The city says we can't drive on it for two weeks. Nothing has been done for weeks. I'll let ya know the schedule moving forward. Thanks, Ron	Jason Rudenick
03/21/2024					
	Generic Activity	Letter delivered	ACT-001255-2024	3yr letter proved to GC, explained process in detail.	Jason Rudenick




Created Date	Activity Type	Activity Name	Activity Number	Activity Comments	Created By
)3/22/2023					
	Generic Activity		ACT-000463-2023	914 Ocean Front E (same as 912), 3/22/23, talked with GC Ron Carrol, he is to call for inspections, also he is working with PW on an alley right of way issue. At this time appears to be fine for 10/14/23 3yr deadline.	Jason Rudenick
04/01/2024					
	Generic Activity		ACT-001382-2024	Emailed 3 year app to gc again after he had received from JR week of 3/21. reminded him of 3 year deadline.	Chad Shelton
04/15/2024					
	Generic Activity		ACT-001566-2024	contractor provided necessary supporting documents for review. Turned app over to SL for review.	Chad Shelton
04/19/2024					
	Generic Activity	Building Official Additional Extension Approved	ACT-001646-2024	3-YEAR CONSTRUCTION TIME LIMIT 365 DAYS TOTAL EXTENSION GRANTED FRO 10/14/2023. PERMIT SHALL EXPIRE ON 10/13/2024 UNLESS AN ADDITIONAL EXTENSION IS GRANTED B' HEARING OFFICER	Tonee Thai
04/08/2024					
	Generic Activity		ACT-001468-2024	Jason met wit GC Ron Carrol 4/9/24. Ron provided status of completion. He is to complete the 3yr Ext request app today. requesting a couple additional months for completion.	Jason Rudenick
04/09/2024					
	Generic Activity		ACT-001494-2024	emailed contractor and homeowner, explained again that they need to fill out the proper extension form, pay fees, and get approved. permits expire 4-11-24. homeowner tried to justify needing an extension via email. explained that this was not adequate to approve the extension.	Chad Shelton

05/06/2024

reated Date	Activity Type	Activity Name	Activity Number	Activity Comments	Created By
	Generic Activity	3-YEAR DEADLINE EXTENSION	ACT-001876-2024	MAILED & EMAILED APPROVED 3-YEAR CONSTRUCTION LIMIT EXTENSION TO PROPERTY OWNER	Debi Schank
7/28/2023					
	Generic Activity	Зуг	ACT-001635-2023	Jason delivered 3yr app to GC, details explained	Jason Rudenick
	Generic Activity	Зуr	ACT-001636-2023	Jason delivered 3yr application to GC, explained in detail.	Jason Rudenick
8/21/2024					
	Generic Activity		ACT-003185-2024	Spoke with GC Ron, he is to call for Finals in the coming weeks. He mentioned will hit 3yr deadline. Stated the custom elevator is on back order.	Jason Rudenick
8/22/2024					
	Generic Activity		ACT-003223-2024	emailed gc with hearing officer extension form.	Chad Shelton
9/11/2023					
	Generic Activity		ACT-001985-2023	Application, letter and fee paid. Application on SL's desk	Jason Rudenick
9/11/2024					
	Generic Activity	Зуг	ACT-003466-2024	Email to GC Ron, he is to provide update for Final inspections.	Jason Rudenick
	Email	3yr update	ACT-003467-2024	Email to GC Ron, he is to provide update for Final inspections.	Jason Rudenick
	Generic Activity		ACT-003468-2024	called gc again and reminded him of upcoming permit expiration. he has received hearing officer extension form and indicated he would be completed by then. working with JR for holds as well.	Chad Shelton
9/13/2023					
	Generic Activity	Application Submitted 09/08/2023	ACT-002006-2023		Tonee Thai
	Generic Activity	Building Official Extension Approved	ACT-002007-2023	3-YEAR CONSTRUCTION TIME LIMIT 180 DAYS TOTAL EXTENSION GRANTED. PERMIT SHALL EXPIRE ON 04/11/2024 UNLESS AN ADDITIONAL EXTENSION IS GRANTED.	Tonee Thai

49 Page 13 of 14

Created Date	Activity Type	Activity Name	Activity Number	Activity Comments	Created By
	Generic Activity	3yr Hearing	ACT-003788-2024	Met with GC, dropped of Hearing App. Gc states the custom elevator is taking longer than expected. Ron (GC). is now to complete the Hearing App process. He understands the urgency.	Jason Rudenick



Attachment No. 3

Building Official Extension

51



CITY OF NEWPORT BEACH COMMUNITY DEVELOPMENT DEPARTMENT BUILDING DIVISION

RECEIVED BY COMMUNITY DEVELOPMENT

100 Civic Center Drive | P.O. Box 1768 | Newport Beach, CA 92658-8915 www.newportbeachca.gov | (949) 644-3200 APR 11 2024

CITY OF NEWPORT BEACH

Three Year Construction Time Limit Extension Building Official Application

Project Address: 914 E. DCCanfront	NB CA		025679
Permit No.: X 2019 - 2085 Original Permit Issued Date:	10.14.20		Date Fee Paid:
PETITIONER/PROPE	ERTY OWNER INFORM	IATION	
Name (Must be payor of fees): Pon Corroll	Company Name: RLCarrollGunk		
Street Address: PD BDX 7829	City: Huntington BC		Zip Code: 92415
Email: RLCarrollgCDgmail.com 714.7490622			
	CT INFORMATION		
Length of extension requested: () MDS .			
New end date if request is approved: 10-1.2024			
Previous Extension(s) Granted? (Y/N): Yes	If Yes, How Many?:		· · ·
Description of Work Under Permit: Mech. permit (HVAc Systen); H2021-0530, E2021-0383,			
Reason for Extension Request OLE AHACHS INC. Due TO ALLEY CONSTRUCTION DUE TO ALLEY CONSTRUCTION PRODUCTION CONSTRUCTION OF TO Portuge N2023-0512			
I HEREBY CERTIFY THAT	T THE ABOVE STATEMEN	IT IS TRUE.	
	Relationship to Property Owner:		Date:
FOR S	TAFF USE ONLY		
Department Action: ⊠Approved □Denied			
Conditions of Approval or Comments: or 10/13/2024 WILLESS ADDITIONAL EXTENSION IS CRAMETED BY HEATING			
Building Inspector Nama:	Signature:		Date:
Reviewed: had Shelfon	Un Or		41/5/24
Approval: Tower (HAT	Signature:	•	Date: 041 191 24

BuildingOfficial3YearExtension Valid Until 04/22/2025 Ordinance 2022-8 / NBMC 15.02.095 - 8-2-23

Date: September 8th, 2023

To: Jason Rudenick Community Development Dep City of Newport Beach (949) 644 -3262

From: Charles Ataii (owner) Ocean Property Rentals, LLC

Property Address: 914 E. Oceanfront, Newport Beach, CA 92653

Mr. Rudenick,

This letter is to confirm the request for the extension of the construction permit for the next 6 months for property address 914 E. Oceanfront, Newport Beach. As the owner of the property, I authorize RLCarroll General Contractors, Inc. to apply for a 6 month extension to permit #2019-2085.

Please let me know if you need any additional information.

Thank you.

P.C. Ataii



April 15, 2024

Jason Rudenick, Building Inspector Community Development 100 Civic Center Drive, 1st Floor, Bay D Newport Beach, CA 2660

Re: 6-month permit extension at 914 E. Oceanfront Permit Number X2019-2085

Dear Jason,

We are requesting a 6-month time extension for the above permit in regard to new construction at 914 E. Oceanfront. There were no provisions provided for this alley on the approved plan for this project.

RL Carroll was hired to construct and complete the alley adjacent to the project. The permit is dated 1/12/24. As alley way construction began, it became evident the 6" high pressure water main was found to have insufficient coverage. This discovery resulted in the need to lower the water main from 910 E. Oceanfront to 918 E. Oceanfront greatly increasing the overall scope of the alley project.

Without the alley access, the project was unable to move forward. It took better than four months to get the alley designed and approved though public works. Please reference Encroachment Permit N2023-0512.

Due to alley construction, 914 E. Oceanfront construction had no access. The elevator company and the appliance company were unable to access the property. They require asphalt or concrete to deliver and install.

Again, due to alley construction, hardscape, site drainage and civil engineering could not begin their phase of construction since the alley grades were not established.

Thank you for your consideration of this extension request.

Sincerely,

Ron Carroll, President RL Carroll General Contractors, Inc.

> P.Q. Box 7829, Huntington Beach, California 92615 (714) 749-0622 • email: rlcarrollgc@gmail.com • CA License #B682756



April 11, 2024

Jason Rudenick, Building Inspector Community Development 100 Civic Center Drive, 1st Floor, Bay D Newport Beach, CA 2660

Re: 6-month permit extension at 914 E. Oceanfront Permit Number X2019-2085

Dear Jason,

We are requesting a 6-month time extension for the above permit in regard to new construction at 914 E. Oceanfront.

RL Carroll was hired to construct and complete the alley way adjacent to the project which has allowed the project to move forward. Please reference Encroachment Permit N2023-0512.

Thank you for your consideration of this extension request.

Sincerely,

Ron Carroll, President RL Carroll General Contractors, Inc.

55



CITY OF NEWPORT BEACH

COMMUNITY DEVELOPMENT DEPARTMENT BUILDING DIVISION

RECEIVED BY COMMUNITY DEVELOPMENT

100 Civic Center Drive | P.O. Box 1768 | Newport Beach, CA 92658-8915 www.newportbeachca.gov | (949) 644-3200 APR 11 2024

CITY OF NEWPORT BEACH

Three Year Construction Time Limit Extension Building Official Application

Project Address: 914 E. Ollanfront	NB CA Receipt No.: /NV-00025679		
Permit No.: X 2019 - 2085 Original Permit Issued Date:	ID.14.20 Extension Fee: Date Fee Paid: \$214 9111124		
PETITIONER/PROPE	RTY OWNER INFORMATION		
Name (Must be payor of fees): <i>P-On Courroll</i>	Company Name: RL Carroll Gunnal Contractors, Inc.		
Street Address: PD BDX 7829	City: State: Zip Code: Hunfington BCh CA 92615		
Email: RLCarroll gCB gmail. com 714.7490622			
	CT INFORMATION		
Length of extension requested: (MDS .			
New end date if request is approved: 10-1-2024			
Previous Extension(s) Granted? (Y/N): Yes	If Yes, How Many?: 1		
Description of Work Under Permit: Mech. permit (HVAc Systen); 42021-0530, E2021-0383,			
Reason for Extension Request	WHAT PRATENCESACIMENT		
	THE ABOVE STATEMENT IS TRUE.		
Petitioners Signature:	Relationship to Property Owner: Date: Gaveral But Marta 2/ 1/1/24		
FOR S	TAFF USE ONLY		
Department Action: ⊠Approved □Den	ied		
of Approval Approval Extension CIEANTED FOR TOTAL OF 365 DAYS FROM			
or Comments: ON 10/13/2024 UNLESS ADDITIONAL EXTENSION IS GRANITED BY HEARING			
Building Inspector Nama: Reviewed:	Signature: Date: 41/5/24		
Building Official Name: Approval:	Signature: Date: Date: Od 1 ig 1 24		

BuildingOfficial3YearExtension Valid Until 04/22/2025 Ordinance 2022-8 / NBMC 15.02.095 - 8-2-23



April 11, 2024

Jason Rudenick, Building Inspector Community Development 100 Civic Center Drive, 1st Floor, Bay D Newport Beach, CA 2660

Re: 6-month permit extension at 914 E. Oceanfront Permit Number X2019-2085

Dear Jason,

We are requesting a 6-month time extension for the above permit in regard to new construction at 914 E. Oceanfront.

RL Carroll was hired to construct and complete the alley way adjacent to the project which has allowed the project to move forward. Please reference Encroachment Permit N2023-0512.

Thank you for your consideration of this extension request.

Sincerely,

Ron Carroll, President RL Carroll General Contractors, Inc.

April 15, 2024

Jason Rudenick, Building Inspector Community Development 100-Civic Center Drive, 1st Floor, Bay D Newport Beach, CA 2660

General Contractors

Re: 6-month permit extension at 914 E. Oceanfront Permit Number X2019-2085

Dear Jason,

We are requesting a 6-month time extension for the above permit in regard to new construction at 914 E. Oceanfront. There were no provisions provided for this alley on the approved plan for this project.

RL Carroll was hired to construct and complete the alley adjacent to the project. The permit is dated 1/12/24. As alley way construction began, it became evident the 6" high pressure water main was found to have insufficient coverage. This discovery resulted in the need to lower the water main from 910 E. Oceanfront to 918 E. Oceanfront greatly increasing the overall scope of the alley project.

Without the alley access, the project was unable to move forward. It took better than four months to get the alley designed and approved though public works. Please reference Encroachment Permit N2023-0512.

Due to alley construction, 914 E. Ocean front construction had no access. The elevator company and the appliance company were unable to access the property. They require asphalt or concrete to deliver and install.

Again, due to alley construction, hardscape, site drainage and civil engineering could not begin their phase of construction since the alley grades were not established.

Thank you for your consideration of this extension request.

Sincerely,

Ron Carroll, President RL Carroll General Contractors, Inc.

> P.Q. Box 7829, Huntington Beach, California 92615 (714) 749-0622 • email: rlcarrollgc@gmail.com • CA License #B682756

> > 58

Date: September 8th, 2023

To: Jason Rudenick Community Development Dep City of Newport Beach (949) 644 -3262

From: Charles Ataii (owner) Ocean Property Rentals, LLC

Property Address: 914 E. Oceanfront, Newport Beach, CA 92653

Mr. Rudenick,

This letter is to confirm the request for the extension of the construction permit for the next 6 months for property address 914 E. Oceanfront, Newport Beach. As the owner of the property, I authorize RLCarroll General Contractors, Inc. to apply for a 6 month extension to permit #2019-2085.

Please let me know if you need any additional information.

Thank you.

P.C. Atali



CITY OF NEWPORT BEACH COMMUNITY DEVELOPMENT DEPARTMENT

RECEIVED BY COMMUNITY DEVELOPMENT

SEP 0.8 2023

100 Civic Center Drive | P.O. Box 1768 | Newport Beach, CA 92658-8915 www.newportbeachca.gov | (949) 644-3200

BUILDING DIVISION

CITY OF NEWPORT BEACH

Three Year Construction Time Limit Extension Building Official Application

Project Address:	914 E. OGER	nufront		Receipt No.:	45
Permit No.:	XZ019-2085	Original Permit Issued Date:	10-14-2020	Extension Fee: \$208 24	
	PETITIO	NER/PROPE	ERTY OWNER INFOR	RMATION	
Name (Must be	payor of fees):		Company Name:	ninin ya kala kanan kata in dala kata yang kata kanan kata kanan kata kata kanan kata kanan kata kanan kata ka	de la de la desenta de la desenta por la desta desenta de la desenta de la desenta de la desenta de la desenta
Street Address:	Ilonx		RLCANNOIL Gen	con Cartoso	brs, Jak
-			City:	State:	Zip Code:
Po Box	7829		Hauthougton Boach Phone:	<u>C</u> A	92615
Email:					
r CArro	llge@grail.	com	714-74	19-0622	
	5-3,	PROJE	CT INFORMATION		
the state of the second s	nsion requested: 6 mc				
New end date i	f request is approved: 🏻 🏠	Apeh 120	324		
	sion(s) Granted? (Y/N):	Nonie	If Yes, How Many?:		
Description of Work Under Permit:	IVEW SINGLE F				
Reason for Extension Request	(Attach Supporting Documents as Needed) COVID 19 matorial & LABOR Shoeting e PROBLEM WHA PUBLIC WORKS ISSUINS A PORMIT to Complete the Alley.				
			THE ABOVE STATEME	ENT IS TRUE.	
Petitioner's Sig	hature:		Relationship to Property Owner:		Date:
PU	allor		General Contracte	n	914723
		FOR S	TAFF USE ONLY		
Department Ac	tion:	Den	ied		
Conditions of Approval or Comments:	180 DAYS OFT 04-11-2024	thistory en	CANTED. PERMUT DITIONAL EXTEN	STHALL EXPI	RE ON'
Building Inspe Reviewed:	Jason	Rudenu	Signature:	2	Date:
Building Officia Approval:	Contraction of the local division of the loc	HA7	Signature	>	Date:

BuildingOfficial3YearExtension Valid Until 04/22/2025 Ordinance 2022-8 / NBMC 15.02.095 - 6-16-22



CITY OF NEWPORT BEACH BUILDING DIVISION

PAID

P.O.BOX 1768, NEWPORT BEACH, CA 92658, (949) 644-3200 SEP 0 8 REC'D

FEE RECEIPT

CITY OF NEWPORT BEACH

	DATE:		
Plan Check #:	Permit #:	Rece	ived by: <u> ∜≻ </u>
Ron Canoll		914 E Quan Fr	m
Payor		Job Address	<u> </u>
Building Plan Check			\$
Harbor Resource Plan Chec	k (Building)		\$
Zoning Plan Check			\$
Grading Plan Check			\$
Fire Plan Check		2330-5055	\$
Electrical Plan Check			\$
Plumbing Plan Check			\$
Mechanical Plan Check			\$
Harbor Resources Plan Che	ck		\$
Overtime Plan Check - Build	ing		\$
Overtime Plan Check - Grad	ing		\$
Overtime Plan Check - Plan	ning		\$
Special Inspection (Lightin	ng) Code Enforcemen	tCDD163	\$
Reinspection B E M P/Spe	cial Inspection	CDD021	\$ 214.00
Reinspection Fire	¹⁹⁹ 1		\$
Temporary Certificate of O	ccupancy	CDD021	\$
Gas Meter Release			\$
Energy Compliance			\$
Planning Department Fees .			\$
Sale of Maps & Publications	(Planning)		\$
Determination of Unreasona	ble Hardship		\$
Public Works Plan Check			\$
Records Management Fee (Copies)	010-2263	\$
Subpoena Fees			\$
Copies/plans/specs			\$
Surety Deposits (Refundable	э)	020-2201	\$
Other (Specify)			\$
••			\$ 2(4,00

 For Plan Check status log on to:

 www.newportbeachca.gov/building,

 select Online Services or call (949) 644-3255

 Fee Receipt No.

 NOTICE: PLAN CHECK EXPIRES 180 DAYS FROM DATE OF SUBMITTAL.

 (Nfeeropt. 04/07/22)



Ron Carroll RLCarroll General Contractors, Inc. PO Box 7829 Huntington Beach, Ca. 92615 September 8, 2023

Mr. Rudenick, **Building Inspector II Community Development** 100 Civic Center Drive, 1st floor bay D, Newport Beach, Ca. 92660

Re: 6-month permit extension at 914 E. Oceanfront X2019-2085

Mr. Rudenick,

We are requesting a 6-month time extension for 914 E. Oceanfront.

Due to Covid 19. Both labor and material were extremely difficult to obtain.

Also, the alley behind both 912 and 914 E. Oceanfront has been tied up in the Public Works department for months. I can't do any site improvements without a Public Works permit.

Ron Carroll

President

62

Date: September 8th, 2023

To: Jason Rudenick Community Development Dep City of Newport Beach (949) 644 -3262

From: Charles Ataii (owner) Ocean Property Rentals, LLC

Property Address: 914 E. Oceanfront, Newport Beach, CA 92653

Mr. Rudenick,

This letter is to confirm the request for the extension of the construction permit for the next 6 months for property address 914 E. Oceanfront, Newport Beach. As the owner of the property, I authorize RLCarroll General Contractors, Inc. to apply for a 6 month extension to permit #2019-2085.

Please let me know if you need any additional information.

Thank you.

P.C. Ataii
